



I. Major Projects Update

Jordan High School Major Renovation

Project Summary:

- Existing facilities built in 1930's and 1940's with additions built in the 1950's through 1990's
- 26.89 acre site
- Existing 301,663 s.f. of permanent and 31,680 s.f. of portable structures
- New and renovated facilities: 395,000 s.f.
- 132 classrooms, six (6) Academies
- Master Plan capacity: 3,600 students

Project Status:

- Ph. 1A Interim Housing: DSA closeout: Underway
- Construction Documents: Ph. 2B Underway
- Schematic Design complete: 2A, 5, 6
- Phase 1B Demolition: Completed
- Phase 1C DSA approval: Completed
- Design Development 2A: Completed
- Ph. 1B Increment 2: Under construction
- Construction Documents 2A: Underway

Upcoming Activities:

- DSA Submittal 2A: August 2015



NTD

Project Team:

- Architect: NTD (Ph. 1, 2B), and PJHM (Ph. 2A, 4, 5, 6)
- Contractors:
 - Phase 1A: McCarthy Building Companies
 - Phase 1B Demo: Unlimited Environmental
 - Phase 1B inc.1: Hayward Baker Inc.
 - Phase 1B inc.2: Pinner Construction Company, Inc.




I. Major Projects Update

Jordan High School Major Renovation

Budgets:

	Phase I	Phase II	Phase IV*	Phase V	Phase VI
Estimated Total Project Budget	\$104M	\$42.6M	\$20.1M	\$18.3M	\$14M
Estimated Construction Budget	\$74M	\$31.7M	\$13.5M	\$14.8M	\$9.8M
Dollars Expended (8/25/14)	\$25.2M	\$235K	\$714.4K	\$126K	\$165K

*AB 300 project

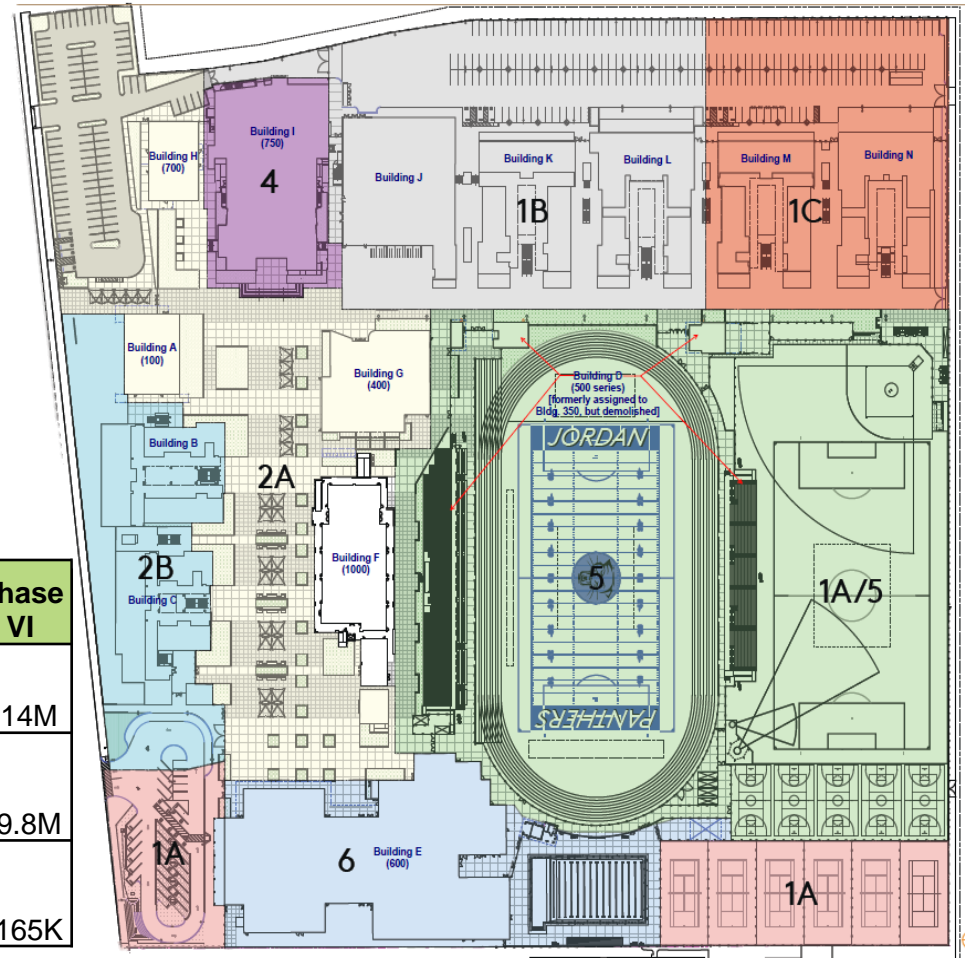



I. Major Projects Update

Jordan High School Major Renovation

