



#### **Project Summary**


- Demolition of gym building identified on the State's AB300 report
- Scope of work: Construction of new physical education building with new locker rooms, fitness lab, and weight room. Addition of new lunch shelter and site work
- Opening Fall 2017

#### **Project Status**

- DSA Agency review: Approved April 2015
- OPSC Conceptual Approval: Complete
- OPSC Funding Approval: Complete
- Bidding: Underway  
Anticipated NTP February 2016

#### **Upcoming Activities**

- Construction: March 2016 – June 2017

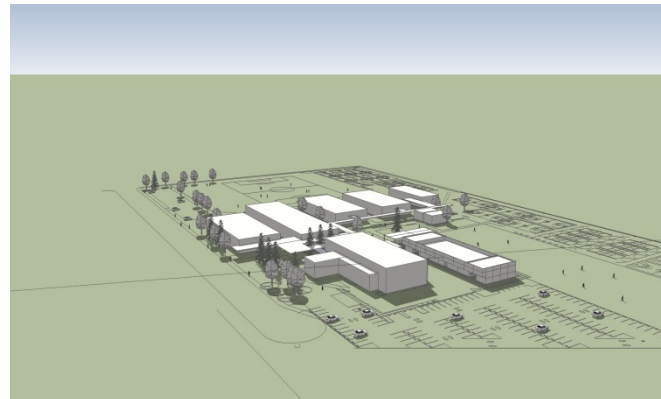

#### **Project Team:**

Architect: LPA, Inc.

Contractor: TBD

#### **Budget:**

- Estimated Total Project Budget: \$7.01M
- Estimated Construction Budget: \$4.60M
- Dollars Expended (as of 01/13/16): \$458K
