



## II. District-Wide Projects Update

### Polytechnic HS Auditorium AB300

#### Project Summary:

- Seismic upgrade to auditorium building identified on the State's AB300 report
- Scope of work is limited to seismic upgrade and subject to confirmation with DSA
- Interim housing (portables) during construction



#### Project Status:

- Construction Anticipated: January 2014
- OPSC Conceptual/Funding Application : Under review
- DSA project approval: Completed June 2, 2014

#### Upcoming Activities:

- Construction Procurement: Underway
- Bid Opening for Interim Housing: September 19, 2014, 2:00 p.m.

#### Project Team:

- Architect: LPA, Inc.


#### Budget:

- Estimated Total Project Budget: \$20.31M
- Estimated Construction Budget: \$14M
- Dollars Expended (as of 8/25/14): \$1.73M



## II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

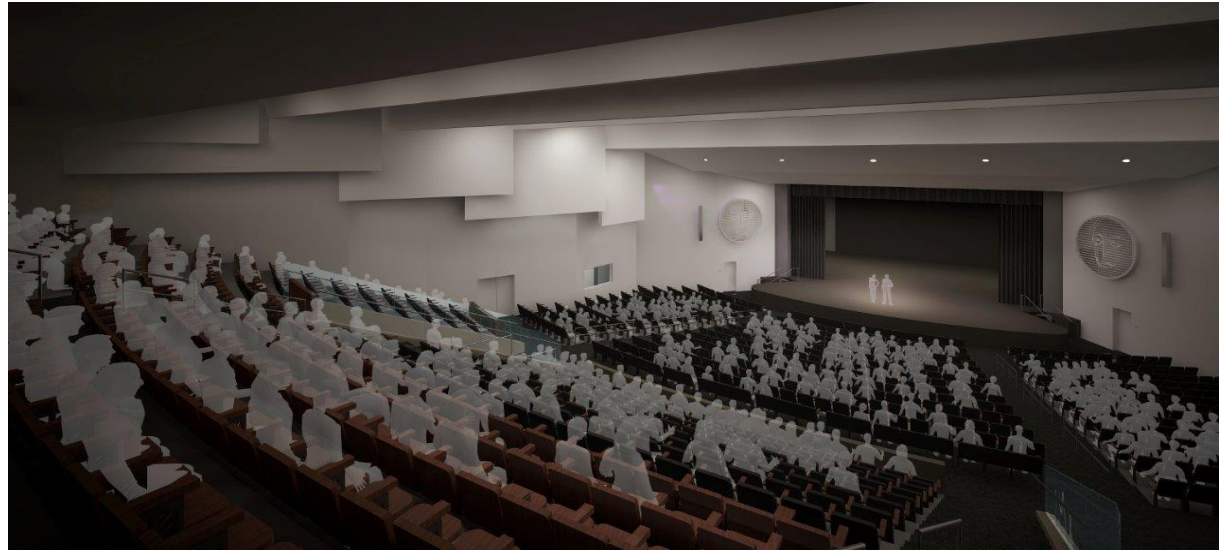

Long Beach Unified School District
