



# I. Major Projects Update

## Jordan High School Major Renovation

### Project Summary:

- Existing facilities built in 1930's and 1940's with additions built in the 1950's through 1990's
- 26.89 acre site
- Existing 301,663 s.f. of permanent and 31,680 s.f. of portable structures
- New and renovated facilities: 395,000 s.f.
- 132 classrooms, six (6) Academies
- Master Plan capacity: 3,600 students

### Project Status:

- Ph. 1A Interim Housing: DSA closeout: Underway
- Construction Documents: Ph. 2B Underway
- Schematic Design complete: 2A, 5, 6
- Phase 1B Demolition: Completed
- Phase 1C DSA approval: Completed

### Upcoming Activities:

- Design Development 2A: Underway
- Design Development AB 300: Completed
- Ph. 1B Increment 1: Completed
- Ph. 1B Increment 2 NTP issued: February 16, 2015



NTD

### Project Team:

- Architect: NTD (Ph. 1, 2B), and PJHM (Ph. 2A, 4, 5, 6)
- Contractors:
  - Phase 1A: McCarthy Building Companies
  - Phase 1B Demo: Unlimited Environmental
  - Phase 1B inc.1: Hayward Baker Inc.
  - Phase 1B inc.2: Pinner Construction Company, Inc.




# I. Major Projects Update

## Jordan High School Major Renovation

### Budgets:

	Phase I	Phase II	Phase IV*	Phase V	Phase VI
<b>Estimated Total Project Budget</b>	\$104M	\$42.6M	\$20.1M	\$18.3M	\$14M
<b>Estimated Construction Budget</b>	\$74M	\$31.7M	\$13.5M	\$14.8M	\$9.8M
<b>Dollars Expended (8/25/14)</b>	\$23.9M	\$235K	\$439K	\$126K	\$165K

\*AB 300 project

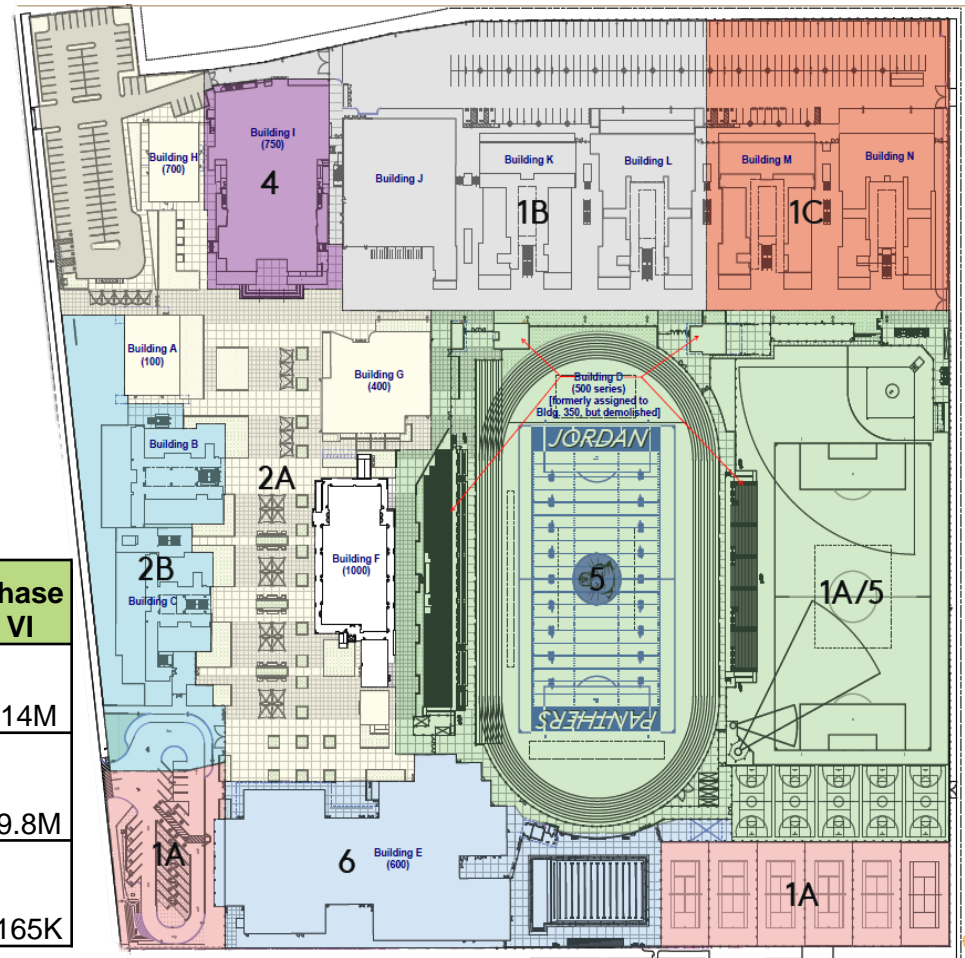



# I. Major Projects Update

## Jordan High School Major Renovation

