



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
<b>State: Active</b>			<b>2/5/18</b>	<b>11/28/24</b>											
<b>Phase: 0EV</b>			<b>8/25/21</b>	<b>12/30/22</b>											
<b>Project Name: EVSS Phase II</b>			<b>8/25/21</b>	<b>12/30/22</b>											
Construction	EVSS Phase II	0EV	8/25/21	12/30/22											
<b>Phase: 0EW</b>			<b>4/1/22</b>	<b>10/31/22</b>											
<b>Project Name: E-Rate - Wireless Upgrade</b>			<b>4/1/22</b>	<b>10/31/22</b>											
Construction	E-Rate - Wireless Upgrade	0EW	4/1/22	10/31/22											
<b>Phase: 0FA</b>			<b>6/1/22</b>	<b>8/23/23</b>											
<b>Project Name: Fire Alarm Phase V - Wilson HS</b>			<b>1/23/23</b>	<b>8/23/23</b>											
Construction	Fire Alarm Phase V - Wilson HS	0FA	1/23/23	8/23/23											
<b>Project Name: Fire Alarms Phase V - Wilson HS</b>			<b>6/1/22</b>	<b>8/31/22</b>											
Construction	Fire Alarms Phase V - Wilson HS	0FA	6/1/22	8/31/22											
<b>Phase: 0TC</b>			<b>7/1/21</b>	<b>6/28/23</b>											
<b>Project Name: Telecom Phase II</b>			<b>7/1/21</b>	<b>6/28/23</b>											
Construction	Telecom Phase II	0TC	7/1/21	6/28/23											
<b>Phase: 2</b>			<b>2/5/18</b>	<b>8/15/22</b>											
<b>Project Name: Kettering ES HVAC</b>			<b>2/5/18</b>	<b>8/15/22</b>											
Construction - Classroom Buildings	Kettering ES HVAC	2	2/5/18	8/14/18											
Owner Move-in - Phase 1	Kettering ES HVAC	2	6/16/18	6/22/18											
Construction - Site Work	Kettering ES HVAC	2	8/15/18	11/14/18											
Owner Move-in - Phase 2	Kettering ES HVAC	2	8/18/18	8/30/18											
Construction - Security Fencing & Water Heater Enclosures	Kettering ES HVAC	2	3/1/19	12/30/20											
Construction - Fire Sprinklers	Kettering ES HVAC	2	6/15/22	8/15/22											
<b>Phase: 3</b>			<b>6/25/18</b>	<b>9/15/21</b>											
<b>Project Name: Lakewood HS HVAC</b>			<b>6/25/18</b>	<b>9/15/21</b>											
Construction - Bldg 200	Lakewood HS HVAC	3	6/25/18	11/16/18											
Owner Move-in - Bldg 200	Lakewood HS HVAC	3	11/17/18	11/21/18											
Construction - Bldgs 300 & 900	Lakewood HS HVAC	3	11/26/18	6/21/19											
Owner Move-in - Bldg 300	Lakewood HS HVAC	3	4/22/19	4/25/19											
Construction - Bldgs 100 & 800 (1st & 3rd floors), Cafeteria	Lakewood HS HVAC	3	6/17/19	8/9/19											
Owner Move-in - Bldg 900	Lakewood HS HVAC	3	6/27/19	6/28/19											
Construction - Bldgs 400 & 800	Lakewood HS HVAC	3	8/5/19	12/31/19											
Owner Move-in - Bldg 100 & Cafeteria	Lakewood HS HVAC	3	8/12/19	8/14/19											
Construction - Bldgs 500 & 800 (2nd & 4th floors)	Lakewood HS HVAC	3	8/16/19	12/20/19											
Construction - Bldg 700	Lakewood HS HVAC	3	9/30/19	2/11/20											
Owner Move-in - 400 & 800 (2ns & 4th floors)	Lakewood HS HVAC	3	12/20/19	1/3/20											
Owner Move-in - Bldgs 500 & 700	Lakewood HS HVAC	3	2/10/20	2/14/20											
	Lakewood HS HVAC	3	10/19/20	9/15/21											
<b>Phase: 4</b>			<b>11/18/19</b>	<b>10/2/23</b>											
<b>Project Name: Jordan HS Ph 2B &amp; 3 (Bldgs 200/300)</b>			<b>7/26/21</b>	<b>10/2/23</b>											
Construction - 2B (Bldg 200)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	7/26/21	5/5/23											
Construction - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	1/26/23	9/22/23											
Owner Move-in - 2B (Bldg 200)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	7/10/23	7/17/23											
Owner Move-in - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	9/25/23	10/2/23											
<b>Project Name: Rogers MS Portables</b>			<b>6/17/20</b>	<b>8/24/22</b>											
Construction	Rogers MS Portables	4	6/17/20	9/4/20											
Owner Move-in	Rogers MS Portables	4	9/7/20	9/11/20											
Construction - Demo Russel Bungalows	Rogers MS Portables	4	6/21/22	8/24/22											
<b>Project Name: Stevenson ES Auditorium Repairs</b>			<b>11/18/19</b>	<b>10/30/20</b>											
Construction - Auditorium	Stevenson ES Auditorium Repairs	4	11/18/19	6/10/20											
Construction - Campuse-wide Fire Alarm Upgrade	Stevenson ES Auditorium Repairs	4	11/18/19	8/21/20											
Construction - Cafeteria/Kitchen	Stevenson ES Auditorium Repairs	4	6/11/20	10/30/20											
Owner Move-in	Stevenson ES Auditorium Repairs	4	8/23/20	8/27/20											
<b>Phase: 5</b>			<b>6/15/20</b>	<b>9/29/22</b>											
<b>Project Name: Lakewood HS Track/Field</b>			<b>2/24/21</b>	<b>5/13/22</b>											
Construction	Lakewood HS Track/Field	5	2/24/21	5/12/22											
Owner Move-in	Lakewood HS Track/Field	5	5/13/22	5/13/22											
<b>Project Name: Madison ES HVAC</b>			<b>7/9/20</b>	<b>8/24/21</b>											

Project updates  
Date: 6/3/22

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction - Phase 1	Madison ES HVAC	5	7/9/20	1/22/21											
Owner Move-in - Phase 1	Madison ES HVAC	5	1/25/21	1/26/21											
Construction - Phase 2	Madison ES HVAC	5	2/1/21	8/18/21											
Owner Move-in - Phase 2	Madison ES HVAC	5	8/19/21	8/24/21											
<b>Project Name: Wilson HS HVAC</b>			<b>6/15/20</b>	<b>9/29/22</b>											
Construction Phase 1 (Bldg 100 North)	Wilson HS HVAC	5	6/15/20	11/20/20											
Construction Phase 2 (Bldg 100 East)	Wilson HS HVAC	5	10/2/20	3/12/21											
Owner Move-in Phase 1 (Bldg 100 North)	Wilson HS HVAC	5	1/4/21	1/6/21											
Construction Phase 3 (Bldg 100 West)	Wilson HS HVAC	5	2/2/21	6/28/21											
Owner Move-in - Phase 2 (Bldg 100 East)	Wilson HS HVAC	5	3/12/21	3/12/21											
Construction Phase 4 (Bldg 200)	Wilson HS HVAC	5	6/18/21	11/4/21											
Owner Move-in Phase 3 (Bldg 100 West)	Wilson HS HVAC	5	6/29/21	7/1/21											
Owner Move-in Phase 4 (Bldg 200)	Wilson HS HVAC	5	10/29/21	11/4/21											
Construction Phase 5 (Bldg 400)	Wilson HS HVAC	5	11/5/21	3/23/22											
Owner Move-in Phase 5 (Bldg 400)	Wilson HS HVAC	5	4/18/22	4/22/22											
Construction Phase 6 (Bldg 300)	Wilson HS HVAC	5	4/18/22	9/22/22											
Construction Phase 7 (Room 510 and Portables)	Wilson HS HVAC	5	6/15/22	8/8/22											
Owner Move-in Phase 7 (Room 510 and Portables)	Wilson HS HVAC	5	8/9/22	8/15/22											
Owner Move-in Phase 6 (Bldg 300)	Wilson HS HVAC	5	9/23/22	9/29/22											
<b>Phase: 6</b>			<b>6/19/20</b>	<b>12/12/22</b>											
<b>Project Name: Bryant ES HVAC</b>			<b>6/15/21</b>	<b>2/9/22</b>											
Construction	Bryant ES HVAC	6	6/15/21	2/9/22											
Owner Move-in - Phase 1	Bryant ES HVAC	6	8/26/21	8/26/21											
Owner Move-in - Phase 2	Bryant ES HVAC	6	12/27/21	12/29/21											
<b>Project Name: Bryant ES Portable Relocations</b>			<b>6/18/21</b>	<b>8/26/21</b>											
Construction	Bryant ES Portable Relocations	6	6/18/21	8/25/21											
Owner Move-in - Phase 1	Bryant ES Portable Relocations	6	8/26/21	8/26/21											
<b>Project Name: Hughes MS HVAC</b>			<b>6/19/20</b>	<b>12/12/22</b>											
Construction - Elect. Upgrades	Hughes MS HVAC	6	6/19/20	1/2/21											
Construction - Kitchen and Cafeteria, and Auditorium	Hughes MS HVAC	6	4/5/21	8/13/21											
Construction - Gym	Hughes MS HVAC	6	6/18/21	5/23/22											
Construction - Bldgs 200/300/600/700 & existing portables	Hughes MS HVAC	6	6/29/21	5/18/22											
Owner Move-in - Kitchen and Cafeteria, and Auditorium	Hughes MS HVAC	6	8/16/21	8/30/21											
Owner Move-in - Bldgs 200/300/600/700 & existing portables	Hughes MS HVAC	6	5/19/22	6/2/22											
Owner Move-in - Gym	Hughes MS HVAC	6	5/24/22	5/24/22											
Construction - Bldgs 100/400/800/900	Hughes MS HVAC	6	5/27/22	12/5/22											
Owner Move-in - Bldgs 100/400/800/900	Hughes MS HVAC	6	12/6/22	12/12/22											
<b>Project Name: Lakewood HS Gym</b>			<b>1/31/22</b>	<b>9/9/22</b>											
Construction	Lakewood HS Gym	6	1/31/22	9/5/22											
Owner Move-in	Lakewood HS Gym	6	9/6/22	9/9/22											
<b>Project Name: Lowell ES Portables</b>			<b>6/18/21</b>	<b>5/31/22</b>											
Construction	Lowell ES Portables	6	6/18/21	5/30/22											
Owner Move-in	Lowell ES Portables	6	5/31/22	5/31/22											
<b>Project Name: Robinson K8 HVAC</b>			<b>8/2/21</b>	<b>8/15/22</b>											
Construction	Robinson K8 HVAC	6	8/2/21	8/1/22											
Owner Move-in	Robinson K8 HVAC	6	8/2/22	8/15/22											
<b>Project Name: Twain ES HVAC</b>			<b>6/21/21</b>	<b>8/29/22</b>											
Construction - HVAC Phase 1	Twain ES HVAC	6	6/21/21	12/24/21											
Owner Move-in - Phase 1	Twain ES HVAC	6	12/26/21	1/5/22											
Construction - HVAC Phase 2	Twain ES HVAC	6	1/6/22	6/20/22											
Owner Move-in - Phase 2	Twain ES HVAC	6	6/21/22	7/4/22											
Construction - Caf� & Kitchen Phase 3	Twain ES HVAC	6	6/22/22	8/24/22											
Owner Move-in Phase 3	Twain ES HVAC	6	8/25/22	8/29/22											
<b>Phase: 7</b>			<b>1/3/22</b>	<b>11/28/24</b>											
<b>Project Name: Avalon K-12 HVAC</b>			<b>1/3/22</b>	<b>8/18/23</b>											
Construction Phase 1 - Bldg G (5000)	Avalon K-12 HVAC	7	1/3/22	8/22/22											
Construction Phase 2 - Bldgs E (7000) & F (6000)	Avalon K-12 HVAC	7	5/1/22	8/25/22											
Construction Phase 3 - Bldg A (1000)	Avalon K-12 HVAC	7	7/5/22	12/12/22											
Owner Move-in Phase 1 Bldg G (5000)	Avalon K-12 HVAC	7	8/19/22	8/23/22											

Project updates  
 Date: 6/3/22

Task  Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Owner Move-in Phase 2 Bldgs E (7000) & F (6000)	Avalon K-12 HVAC	7	8/26/22	9/1/22											
Owner Move-in Phase 3 Bldg A (1000)	Avalon K-12 HVAC	7	12/13/22	1/12/23											
Construction Phase 4 - Bldgs B (3000) & D (4000)	Avalon K-12 HVAC	7	12/28/22	7/24/23											
Construction Phase 5B - Portables	Avalon K-12 HVAC	7	6/19/23	8/18/23											
Owner Move-in Phase 4 Bldgs B (3000) & D (4000)	Avalon K-12 HVAC	7	7/25/23	8/7/23											
<b>Project Name: Bancroft MS HVAC</b>			<b>4/20/22</b>	<b>8/31/23</b>											
Construction	Bancroft MS HVAC	7	4/20/22	8/28/23											
Owner Move-in	Bancroft MS HVAC	7	8/29/23	8/31/23											
<b>Project Name: Hamilton MS Gym Measure K</b>			<b>4/13/23</b>	<b>11/28/24</b>											
Construction - Gym	Hamilton MS Gym Measure K	7	4/13/23	11/20/24											
Construction - Restore Site Paving & Striping	Hamilton MS Gym Measure K	7	8/29/24	11/20/24											
Owner Move-in	Hamilton MS Gym Measure K	7	11/25/24	11/28/24											
<b>Project Name: Holmes ES HVAC</b>			<b>4/13/22</b>	<b>8/21/23</b>											
Construction - Phase 1	Holmes ES HVAC	7	4/13/22	11/11/22											
Owner Move-in - Phase 1	Holmes ES HVAC	7	11/14/22	11/18/22											
Construction - Phase 2	Holmes ES HVAC	7	11/21/22	3/31/23											
Owner Move-in - Phase 2	Holmes ES HVAC	7	4/3/23	4/7/23											
Construction - Phase 3	Holmes ES HVAC	7	4/10/23	8/14/23											
Owner Move-in - Phase 3	Holmes ES HVAC	7	8/15/23	8/21/23											
<b>Project Name: Keller MS New Locker Room</b>			<b>6/13/22</b>	<b>6/23/23</b>											
Construction	Keller MS New Locker Room	7	6/13/22	6/9/23											
Owner Move-in	Keller MS New Locker Room	7	6/12/23	6/23/23											
<b>Phase: 8</b>			<b>6/15/22</b>	<b>9/23/24</b>											
<b>Project Name: Avalon K-12 Ball Field</b>			<b>12/26/22</b>	<b>8/8/23</b>											
Construction	Avalon K-12 Ball Field	8	12/26/22	8/1/23											
Owner Move-in	Avalon K-12 Ball Field	8	8/2/23	8/8/23											
<b>Project Name: Birney ES Modernization</b>			<b>6/15/22</b>	<b>6/19/24</b>											
Construction - SCE Upgrades	Birney ES Modernization	8	6/15/22	9/1/22											
Construction - HVAC Summer Phase	Birney ES Modernization	8	6/15/23	8/25/23											
Construction - HVAC Phase 1	Birney ES Modernization	8	6/15/23	1/1/24											
Owner Move-in - Summer Phase	Birney ES Modernization	8	8/28/23	9/1/23											
Owner Move-in - Phase 1	Birney ES Modernization	8	1/2/24	1/8/24											
Construction HVAC Phase 2	Birney ES Modernization	8	1/2/24	6/12/24											
Owner Move-in - Phase 2	Birney ES Modernization	8	6/13/24	6/19/24											
<b>Project Name: Emerson ES Modernization</b>			<b>6/19/23</b>	<b>7/15/24</b>											
Construction	Emerson ES Modernization	8	6/19/23	7/1/24											
Owner Move-in	Emerson ES Modernization	8	7/2/24	7/15/24											
<b>Project Name: Gompers K8 Modernization</b>			<b>6/19/23</b>	<b>7/11/24</b>											
Construction - HVAC Phase 1	Gompers K8 Modernization	8	6/19/23	12/20/23											
Owner Move-in - Phase 1	Gompers K8 Modernization	8	12/21/23	1/4/24											
Construction - HVAC Phase 2	Gompers K8 Modernization	8	1/5/24	6/27/24											
Owner Move-in - Final Move-in	Gompers K8 Modernization	8	6/28/24	7/11/24											
<b>Project Name: Lakewood HS Portables</b>			<b>6/17/23</b>	<b>8/28/23</b>											
Construction	Lakewood HS Portables	8	6/17/23	8/28/23											
<b>Project Name: Stanford MS Interim Housing</b>			<b>1/1/23</b>	<b>8/31/23</b>											
Construction	Stanford MS Interim Housing	8	1/1/23	8/31/23											
<b>Project Name: Wilson HS Aquatic Center</b>			<b>6/16/23</b>	<b>9/23/24</b>											
Construction	Wilson HS Aquatic Center	8	6/16/23	9/16/24											
Owner Move-in	Wilson HS Aquatic Center	8	9/17/24	9/23/24											
<b>State: Complete</b>			<b>10/1/14</b>	<b>11/29/21</b>											
<b>Phase: 0A</b>			<b>8/1/19</b>	<b>9/30/21</b>											
<b>Project Name: AV Portables Phase I</b>			<b>8/1/19</b>	<b>3/27/20</b>											
Construction	AV Portables Phase I	0A	8/1/19	3/27/20											
<b>Project Name: AV Portables Phase II</b>			<b>6/15/20</b>	<b>8/21/20</b>											
Construction	AV Portables Phase II	0A	6/15/20	8/21/20											
<b>Project Name: AV Portables Phase III</b>			<b>3/4/21</b>	<b>9/30/21</b>											
Construction	AV Portables Phase III	0A	3/4/21	9/30/21											
<b>Phase: OFA</b>			<b>6/30/16</b>	<b>7/30/21</b>											

Project updates  
Date: 6/3/22

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
<b>Project Name: Fire Alarms/Life Safety Sys - Phase II</b>			<b>6/30/16</b>	<b>6/30/17</b>	Project Name: Fire Alarms/Life Safety Sys - Phase II										
Construction	Fire Alarms/Life Safety Sys - Phase II	OFA	6/30/16	6/30/17											
<b>Project Name: Fire Alarms/Life Safety Sys - Phase III</b>			<b>7/20/17</b>	<b>9/14/18</b>	Project Name: Fire Alarms/Life Safety Sys - Phase III										
Construction - Monroe	Fire Alarms/Life Safety Sys - Phase III	OFA	7/20/17	12/31/17											
Construction - Marshall	Fire Alarms/Life Safety Sys - Phase III	OFA	9/1/17	9/14/18											
Construction - Cubberly/King	Fire Alarms/Life Safety Sys - Phase III	OFA	9/1/17	9/14/18											
<b>Project Name: Fire Alarms/Life Safety Sys - Phase IV</b>			<b>12/10/18</b>	<b>1/31/20</b>	Project Name: Fire Alarms/Life Safety Sys - Phase IV										
Construction	Fire Alarms/Life Safety Sys - Phase IV	OFA	12/10/18	1/31/20											
<b>Project Name: Fire Alarms/Life Safety Sys - Phase V</b>			<b>3/10/20</b>	<b>7/30/21</b>	Project Name: Fire Alarms/Life Safety Sys - Phase V										
Construction	Fire Alarms/Life Safety Sys - Phase V	OFA	3/10/20	7/30/21											
<b>Phase: OICS</b>			<b>8/1/16</b>	<b>5/7/21</b>	Phase: OICS										
<b>Project Name: ICS</b>			<b>8/1/16</b>	<b>10/15/20</b>	Project Name: ICS										
Construction	ICS	OICS	8/1/16	10/15/20											
<b>Project Name: ICS Phase II</b>			<b>2/4/21</b>	<b>5/7/21</b>	Project Name: ICS Phase II										
Construction	ICS Phase II	OICS	2/4/21	5/7/21											
<b>Project Name: Jordan HS ICS</b>			<b>10/8/20</b>	<b>3/31/21</b>	Project Name: Jordan HS ICS										
Construction	Jordan HS ICS	OICS	10/8/20	3/31/21											
<b>Phase: OS</b>			<b>8/22/18</b>	<b>2/28/20</b>	Phase: OS										
<b>Project Name: Security Improvements</b>			<b>8/22/18</b>	<b>2/28/20</b>	Project Name: Security Improvements										
Construction	Security Improvements	OS	8/22/18	2/28/20											
<b>Phase: OSC</b>			<b>7/6/17</b>	<b>1/30/18</b>	Phase: OSC										
<b>Project Name: Security Camera Phase II</b>			<b>7/6/17</b>	<b>1/30/18</b>	Project Name: Security Camera Phase II										
Construction	Security Camera Phase II	OSC	7/6/17	1/30/18											
<b>Phase: OW</b>			<b>9/22/17</b>	<b>8/31/18</b>	Phase: OW										
<b>Project Name: E Rate 2016 / 2017</b>			<b>9/22/17</b>	<b>8/31/18</b>	Project Name: E Rate 2016 / 2017										
Construction	E Rate 2016 / 2017	OW	9/22/17	8/31/18											
<b>Project Name: Wireless Phase V</b>			<b>1/4/18</b>	<b>4/4/18</b>	Project Name: Wireless Phase V										
Construction	Wireless Phase V	OW	1/4/18	4/4/18											
<b>Phase: 1</b>			<b>10/1/14</b>	<b>1/29/21</b>	Phase: 1										
<b>Project Name: Barton/Educare ES</b>			<b>2/24/17</b>	<b>7/3/18</b>	Project Name: Barton/Educare ES										
Construction	Barton/Educare ES	1	2/24/17	5/17/18											
Owner Move-in	Barton/Educare ES	1	7/2/18	7/3/18											
<b>Project Name: Browning HS New Construction</b>			<b>10/1/14</b>	<b>5/28/19</b>	Project Name: Browning HS New Construction										
Construction	Browning HS New Construction	1	10/1/14	12/28/17											
Owner Move-in	Browning HS New Construction	1	7/31/17	1/11/18											
Additional Construction - Site and off-site Work	Browning HS New Construction	1	12/29/17	5/28/19											
<b>Project Name: Cabrillo HS Track/Field</b>			<b>6/15/17</b>	<b>11/28/17</b>	Project Name: Cabrillo HS Track/Field										
Construction	Cabrillo HS Track/Field	1	6/15/17	10/26/17											
Owner Move-in	Cabrillo HS Track/Field	1	11/14/17	11/28/17											
<b>Project Name: Head Start at Bethune</b>			<b>3/8/18</b>	<b>5/14/18</b>	Project Name: Head Start at Bethune										
Construction	Head Start at Bethune	1	3/8/18	5/4/18											
Owner Move-in	Head Start at Bethune	1	5/8/18	5/14/18											
<b>Project Name: Head Start at Hudson</b>			<b>10/23/17</b>	<b>4/12/18</b>	Project Name: Head Start at Hudson										
Construction	Head Start at Hudson	1	10/23/17	4/11/18											
Owner Move-in	Head Start at Hudson	1	4/12/18	4/12/18											
<b>Project Name: Head Start at Jordan Plus</b>			<b>10/24/17</b>	<b>5/8/18</b>	Project Name: Head Start at Jordan Plus										
Construction	Head Start at Jordan Plus	1	10/24/17	5/7/18											
Owner Move-in	Head Start at Jordan Plus	1	5/8/18	5/8/18											
<b>Project Name: Jordan HS Ph 1C, 1D &amp; 4</b>			<b>10/18/17</b>	<b>1/29/21</b>	Project Name: Jordan HS Ph 1C, 1D & 4										
Construction - Phase 1C & 1D	Jordan HS Ph 1C, 1D & 4	1	10/18/17	12/20/19											
Construction - Phase 4	Jordan HS Ph 1C, 1D & 4	1	10/18/17	1/29/21											
Owner Move-in Phase 1C (Bldgs 1400 & 1500)	Jordan HS Ph 1C, 1D & 4	1	12/21/19	1/3/20											
Owner Move-in Phase 4	Jordan HS Ph 1C, 1D & 4	1	12/1/20	12/1/20											
<b>Project Name: Kettering ES Interim Housing</b>			<b>10/19/17</b>	<b>2/20/18</b>	Project Name: Kettering ES Interim Housing										
Construction	Kettering ES Interim Housing	1	10/19/17	2/20/18											
Owner Move-in	Kettering ES Interim Housing	1	12/16/17	1/3/18											
<b>Project Name: Monroe K8 Interim Housing</b>			<b>7/21/17</b>	<b>12/26/17</b>	Project Name: Monroe K8 Interim Housing										
Construction	Monroe K8 Interim Housing	1	7/21/17	12/11/17											

Project updates  
 Date: 6/3/22

Task Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Owner Move-in	Monroe K8 Interim Housing	1	12/22/17	12/26/17											
<b>Project Name: Poly HS ADA Improvements</b>			<b>6/19/17</b>	<b>9/28/18</b>											
Construction	Poly HS ADA Improvements	1	6/19/17	9/28/18											
<b>Project Name: Poly HS Auditorium</b>			<b>1/6/15</b>	<b>11/2/17</b>											
Construction	Poly HS Auditorium	1	1/6/15	10/26/17											
Owner Move-in	Poly HS Auditorium	1	10/23/17	11/2/17											
<b>Project Name: Poly HS Band Bldg Conversion Work</b>			<b>10/23/17</b>	<b>11/16/17</b>											
Construction	Poly HS Band Bldg Conversion Work	1	10/23/17	11/14/17											
Owner Move-in	Poly HS Band Bldg Conversion Work	1	11/15/17	11/16/17											
<b>Project Name: Renaissance HS</b>			<b>9/6/16</b>	<b>1/4/19</b>											
Construction	Renaissance HS	1	9/6/16	1/4/19											
Owner Move-in	Renaissance HS	1	7/16/18	7/16/18											
<b>Project Name: Riley ES Interim Housing</b>			<b>10/20/17</b>	<b>12/28/17</b>											
Construction	Riley ES Interim Housing	1	10/20/17	12/22/17											
Owner Move-in	Riley ES Interim Housing	1	12/27/17	12/28/17											
<b>Project Name: Rogers MS Interim Housing</b>			<b>10/16/17</b>	<b>12/31/17</b>											
Construction	Rogers MS Interim Housing	1	10/16/17	12/7/17											
Owner Move-in	Rogers MS Interim Housing	1	12/29/17	12/31/17											
<b>Project Name: Sato HS Conversion</b>			<b>6/5/17</b>	<b>9/8/17</b>											
Construction	Sato HS Conversion	1	6/5/17	9/8/17											
Owner Move-in	Sato HS Conversion	1	8/1/17	8/18/17											
<b>Project Name: Sato HS Gym</b>			<b>5/23/16</b>	<b>1/31/18</b>											
Construction	Sato HS Gym	1	5/23/16	1/31/18											
Owner Move-in	Sato HS Gym	1	8/21/17	1/8/18											
<b>Project Name: Wilson HS Auditorium</b>			<b>2/22/16</b>	<b>3/6/18</b>											
Construction	Wilson HS Auditorium	1	2/22/16	2/19/18											
Owner Move-in	Wilson HS Auditorium	1	2/21/18	3/6/18											
<b>Project Name: Wilson HS Track/Field</b>			<b>9/18/17</b>	<b>4/9/18</b>											
Construction	Wilson HS Track/Field	1	9/18/17	3/30/18											
Owner Move-in	Wilson HS Track/Field	1	4/3/18	4/9/18											
<b>Phase: 2</b>			<b>12/20/17</b>	<b>9/4/20</b>											
<b>Project Name: Cleveland ES HVAC</b>			<b>1/3/18</b>	<b>8/23/18</b>											
Construction	Cleveland ES HVAC	2	1/3/18	8/13/18											
Owner Move-in	Cleveland ES HVAC	2	8/21/18	8/23/18											
<b>Project Name: Garfield ES HVAC</b>			<b>2/6/18</b>	<b>11/16/18</b>											
Construction - Phase 1 (Site, Bldgs C & E)	Garfield ES HVAC	2	2/6/18	7/13/18											
Construction - Phase 2 (Bldgs A, D, & F)	Garfield ES HVAC	2	7/16/18	8/24/18											
Owner Move-in - Phase 1	Garfield ES HVAC	2	8/13/18	8/18/18											
Owner Move-in - Phase 2	Garfield ES HVAC	2	8/20/18	8/28/18											
Construction - Phase 3	Garfield ES HVAC	2	8/27/18	11/16/18											
Owner Move-in - Phase 3	Garfield ES HVAC	2	10/20/18	10/20/18											
<b>Project Name: Poly HS Track/Field</b>			<b>12/20/17</b>	<b>9/10/18</b>											
Construction	Poly HS Track/Field	2	12/20/17	9/10/18											
Owner Move-in	Poly HS Track/Field	2	9/10/18	9/10/18											
<b>Project Name: Riley ES HVAC</b>			<b>1/3/18</b>	<b>12/23/18</b>											
Construction - Classroom Building	Riley ES HVAC	2	1/3/18	8/10/18											
Construction - Site Work	Riley ES HVAC	2	8/11/18	12/23/18											
Owner Move-in	Riley ES HVAC	2	8/14/18	8/20/18											
<b>Project Name: Rogers MS HVAC</b>			<b>2/12/18</b>	<b>9/4/20</b>											
Construction	Rogers MS HVAC	2	2/12/18	8/14/18											
Owner Move-in	Rogers MS HVAC	2	8/15/18	8/27/18											
Construction - Locker Room	Rogers MS HVAC	2	6/20/20	9/4/20											
<b>Project Name: Rogers MS Track/Field</b>			<b>6/18/18</b>	<b>8/27/18</b>											
Construction	Rogers MS Track/Field	2	6/18/18	8/24/18											
Owner Move-in	Rogers MS Track/Field	2	8/27/18	8/27/18											
<b>Project Name: Stephens MS HVAC</b>			<b>2/9/18</b>	<b>8/30/18</b>											
Construction	Stephens MS HVAC	2	2/9/18	8/17/18											
Owner Move-in (furniture)	Stephens MS HVAC	2	7/23/18	8/30/18											
Owner Move-in - final	Stephens MS HVAC	2	8/13/18	8/18/18											

Project updates  
Date: 6/3/22

Task Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT**  
**EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
<b>Project Name: Stephens MS Track/Field</b>			<b>4/16/18</b>	<b>9/18/18</b>											
Construction	Stephens MS Track/Field	2	4/16/18	9/17/18											
Owner Move-in	Stephens MS Track/Field	2	9/18/18	9/18/18											
<b>Project Name: Webster ES Interim Housing</b>			<b>1/3/18</b>	<b>8/11/18</b>											
Construction	Webster ES Interim Housing	2	1/3/18	7/30/18											
Owner Move-in	Webster ES Interim Housing	2	7/31/18	8/11/18											
<b>Phase: 3</b>			<b>6/11/18</b>	<b>11/29/21</b>											
<b>Project Name: Barton ES HVAC</b>			<b>6/18/18</b>	<b>8/25/19</b>											
Construction - Phase 1	Barton ES HVAC	3	6/18/18	12/21/18											
Owner Move-in Phase 1	Barton ES HVAC	3	12/31/18	1/2/19											
Construction - Phase 2	Barton ES HVAC	3	1/3/19	6/19/19											
Owner Move-in Phase 2	Barton ES HVAC	3	6/19/19	6/21/19											
Construction - Phase 3	Barton ES HVAC	3	6/22/19	8/20/19											
Owner Move-in Phase 3	Barton ES HVAC	3	8/21/19	8/25/19											
<b>Project Name: Burcham ES HVAC</b>			<b>6/25/18</b>	<b>9/25/19</b>											
Construction	Burcham ES HVAC	3	6/25/18	9/25/19											
Owner Move-in - Phase 1	Burcham ES HVAC	3	1/2/19	1/18/19											
Owner Move-in - Phase 2	Burcham ES HVAC	3	7/29/19	7/31/19											
Owner Move-in - Phase 3	Burcham ES HVAC	3	8/26/19	8/26/19											
<b>Project Name: Jefferson MS HVAC</b>			<b>9/10/18</b>	<b>6/30/20</b>											
Construction	Jefferson MS HVAC	3	9/10/18	8/26/19											
Construction - elevator	Jefferson MS HVAC	3	5/1/19	6/30/20											
Owner Move-in	Jefferson MS HVAC	3	8/22/19	8/26/19											
<b>Project Name: Jefferson MS Track/Field</b>			<b>12/1/18</b>	<b>8/25/19</b>											
Construction	Jefferson MS Track/Field	3	12/1/18	8/25/19											
Owner Move-in	Jefferson MS Track/Field	3	8/21/19	8/25/19											
<b>Project Name: Jordan HS Ph 2A (Bldgs 100/400)</b>			<b>10/25/18</b>	<b>10/14/20</b>											
Construction	Jordan HS Ph 2A (Bldgs 100/400)	3	10/25/18	9/30/20											
Owner Move-in (Bldg 100)	Jordan HS Ph 2A (Bldgs 100/400)	3	12/21/19	1/3/20											
Owner Move-in (Bldg 400)	Jordan HS Ph 2A (Bldgs 100/400)	3	10/13/20	10/14/20											
<b>Project Name: Keller MS Conversion</b>			<b>9/12/18</b>	<b>4/26/19</b>											
Construction	Keller MS Conversion	3	9/12/18	4/25/19											
Owner Move-in - Phase 1	Keller MS Conversion	3	4/25/19	4/26/19											
<b>Project Name: Keller MS HVAC</b>			<b>9/12/18</b>	<b>8/20/19</b>											
Construction	Keller MS HVAC	3	9/12/18	8/19/19											
Owner Move-in - Phase 1	Keller MS HVAC	3	4/25/19	4/28/19											
Owner Move-in - Phase 2	Keller MS HVAC	3	8/20/19	8/20/19											
<b>Project Name: Lindsey MS HVAC (Bldg D)</b>			<b>6/18/18</b>	<b>1/2/19</b>											
Construction	Lindsey MS HVAC (Bldg D)	3	6/18/18	12/21/18											
Owner Move-in	Lindsey MS HVAC (Bldg D)	3	1/2/19	1/2/19											
<b>Project Name: Longfellow ES HVAC</b>			<b>6/18/18</b>	<b>8/27/20</b>											
Construction - Auditorium	Longfellow ES HVAC	3	6/18/18	8/11/18											
Construction - CR Bldgs 1000 & 2000	Longfellow ES HVAC	3	7/2/18	4/26/19											
Owner Move-In - Auditorium	Longfellow ES HVAC	3	8/12/18	8/16/18											
Construction - CR Bldgs 3000 & 4000	Longfellow ES HVAC	3	4/22/19	8/13/19											
Construction - Kindergarten Rooms	Longfellow ES HVAC	3	4/22/19	10/29/19											
Owner Move-in - CR Bldgs 1000 & 2000	Longfellow ES HVAC	3	4/24/19	4/28/19											
Owner Move-in - CR Bldgs 3000 & 4000	Longfellow ES HVAC	3	8/14/19	8/18/19											
Owner Move-in - Kindergarten Rooms	Longfellow ES HVAC	3	11/25/19	11/29/19											
Construction - Kitchen	Longfellow ES HVAC	3	6/18/20	8/27/20											
Owner Move-in - Kitchen	Longfellow ES HVAC	3	8/27/20	8/27/20											
<b>Project Name: Lowell ES HVAC</b>			<b>9/10/18</b>	<b>11/29/21</b>											
Construction	Lowell ES HVAC	3	9/10/18	8/25/19											
Owner Move-in (Classrooms building)	Lowell ES HVAC	3	6/14/19	6/20/19											
Construction - Aud/Cafeteria Bldgs	Lowell ES HVAC	3	6/17/19	11/27/19											
Owner Move-in (Non-Classrooms)	Lowell ES HVAC	3	8/21/19	8/25/19											
Owner Move-In Aud/Cafeteria Bldgs	Lowell ES HVAC	3	11/28/19	12/4/19											
Construction - Stage Lift	Lowell ES HVAC	3	6/15/21	11/29/21											
<b>Project Name: MacArthur ES HVAC</b>			<b>6/25/18</b>	<b>8/21/19</b>											
Construction	MacArthur ES HVAC	3	6/25/18	8/21/19											

Project updates  
 Date: 6/3/22

Task  Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction - Bldgs B & C	MacArthur ES HVAC	3	6/25/18	1/2/19											
Construction - Bldg A	MacArthur ES HVAC	3	12/24/18	4/19/19											
Owner Move-in Bldgs B & C	MacArthur ES HVAC	3	1/2/19	1/4/19											
Owner Move-in Bldg A	MacArthur ES HVAC	3	4/20/19	4/23/19											
Construction - Bldg D	MacArthur ES HVAC	3	4/24/19	8/16/19											
Construction - Bldg E	MacArthur ES HVAC	3	6/13/19	8/19/19											
Owner Move-in Bldgs D & E	MacArthur ES HVAC	3	8/17/19	8/21/19											
<b>Project Name: Mann ES HVAC</b>			<b>9/4/18</b>	<b>8/19/19</b>											
Construction	Mann ES HVAC	3	9/4/18	8/18/19											
Owner Move-in - Phase 1	Mann ES HVAC	3	4/19/19	4/24/19											
Owner Move-in - Phase 2	Mann ES HVAC	3	8/17/19	8/19/19											
<b>Project Name: McKinley ES HVAC</b>			<b>6/18/18</b>	<b>7/3/19</b>											
Construction Phase 1	McKinley ES HVAC	3	6/18/18	12/21/18											
Owner Move-in Phase 1	McKinley ES HVAC	3	12/26/18	12/27/18											
Construction Phase 2	McKinley ES HVAC	3	12/28/18	7/1/19											
Owner Move-in Phase 2	McKinley ES HVAC	3	7/1/19	7/3/19											
<b>Project Name: Millikan HS New 1000 Bldg</b>			<b>12/3/18</b>	<b>8/28/20</b>											
Construction	Millikan HS New 1000 Bldg	3	12/3/18	8/3/20											
Owner Move-in	Millikan HS New 1000 Bldg	3	8/26/20	8/28/20											
<b>Project Name: Poly HS Bleachers and Field Lighting</b>			<b>12/21/18</b>	<b>9/5/19</b>											
Construction - Soil Remediation	Poly HS Bleachers and Field Lighting	3	12/21/18	1/4/19											
Construction	Poly HS Bleachers and Field Lighting	3	1/22/19	9/5/19											
<b>Project Name: Sato HS New Bldg</b>			<b>6/11/18</b>	<b>8/19/19</b>											
Construction	Sato HS New Bldg	3	6/11/18	8/12/19											
Owner Move-in	Sato HS New Bldg	3	8/13/19	8/19/19											
<b>Project Name: Webster ES HVAC</b>			<b>8/27/18</b>	<b>8/20/19</b>											
Construction - Phase 1	Webster ES HVAC	3	8/27/18	5/31/19											
Construction - Auditorium	Webster ES HVAC	3	4/22/19	8/16/19											
Construction - Cafeteria/Kitchen	Webster ES HVAC	3	6/15/19	8/20/19											
Owner Move-in Phase 1	Webster ES HVAC	3	8/17/19	8/17/19											
Owner Move-in Auditorium/Café/Kitchen	Webster ES HVAC	3	8/17/19	8/18/19											
<b>Phase: 4</b>			<b>6/14/19</b>	<b>11/30/20</b>											
<b>Project Name: Alvarado ES HVAC</b>			<b>7/22/19</b>	<b>7/24/20</b>											
Construction	Alvarado ES HVAC	4	7/22/19	7/10/20											
Owner Move-in	Alvarado ES HVAC	4	7/13/20	7/24/20											
<b>Project Name: Bixby ES HVAC</b>			<b>6/14/19</b>	<b>7/21/20</b>											
Construction	Bixby ES HVAC	4	6/14/19	7/17/20											
Owner Move-in - Phase 1	Bixby ES HVAC	4	8/20/19	8/29/19											
Owner Move-in - Phase 2	Bixby ES HVAC	4	11/25/19	11/27/19											
Owner Move-in - Phase 3	Bixby ES HVAC	4	2/29/20	2/29/20											
Owner Move-in - Phase 4	Bixby ES HVAC	4	7/20/20	7/21/20											
<b>Project Name: Hughes MS Portables</b>			<b>6/20/19</b>	<b>9/2/20</b>											
Construction - AC Paving	Hughes MS Portables	4	6/20/19	8/22/19											
Construction - Portable Installation	Hughes MS Portables	4	4/13/20	4/17/20											
Construction - Electrical and Low Voltage work	Hughes MS Portables	4	6/15/20	9/1/20											
Owner Move-in	Hughes MS Portables	4	9/2/20	9/2/20											
<b>Project Name: Millikan HS Track/Field</b>			<b>1/2/20</b>	<b>11/30/20</b>											
Construction	Millikan HS Track/Field	4	1/2/20	11/27/20											
Owner Move-in	Millikan HS Track/Field	4	11/30/20	11/30/20											
<b>Project Name: Muir K8 HVAC</b>			<b>8/12/19</b>	<b>8/25/20</b>											
Construction - Bldgs B & C	Muir K8 HVAC	4	8/12/19	12/20/19											
Owner Move-in - Bldgs B & C	Muir K8 HVAC	4	12/26/19	12/31/19											
Construction - Bldg D	Muir K8 HVAC	4	1/1/20	7/20/20											
Construction - Bldg A	Muir K8 HVAC	4	5/4/20	8/23/20											
Owner Move-in - Bldg A	Muir K8 HVAC	4	8/12/20	8/14/20											
Owner Move-in - Bldg D	Muir K8 HVAC	4	8/24/20	8/25/20											
<b>Project Name: Naples ES Modernization</b>			<b>10/3/19</b>	<b>7/13/20</b>											
Construction - Bldg 100	Naples ES Modernization	4	10/3/19	5/15/20											
Construction - Bldg 200	Naples ES Modernization	4	10/3/19	5/15/20											


Project updates  
Date: 6/3/22

Task  Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT  
EXECUTIVE PROGRAM SCHEDULE (up to Phase 8 projects) as of 4/30/2022**

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Construction - Bldg 200 Lobby	Naples ES Modernization	4	3/16/20	5/15/20											
Construction - Bldg 300	Naples ES Modernization	4	3/26/20	6/29/20											
Owner Move-in Bldg 100	Naples ES Modernization	4	5/23/20	5/23/20											
Owner Move-in Bldgs 200 and 300	Naples ES Modernization	4	6/30/20	7/13/20											
<b>Project Name: Stephens MS Site Improvements</b>			<b>8/22/19</b>	<b>7/2/20</b>											
Construction	Stephens MS Site Improvements	4	8/22/19	12/20/19											
Owner Move-in	Stephens MS Site Improvements	4	6/15/20	7/2/20											
<b>Phase: 5</b>			<b>3/23/20</b>	<b>8/6/21</b>											
<b>Project Name: Cubberley K8 Modernization</b>			<b>4/29/20</b>	<b>7/16/21</b>											
Construction - Ph. 1 (Bldg E)	Cubberley K8 Modernization	5	4/29/20	8/21/20											
Construction - Ph. 2 (Bldgs A & B)	Cubberley K8 Modernization	5	6/1/20	12/21/20											
Construction - Ph. 3 (Bldg C)	Cubberley K8 Modernization	5	6/22/20	1/21/21											
Owner Move-in - Bldg E	Cubberley K8 Modernization	5	8/24/20	8/24/20											
Owner Move-in Bldg A	Cubberley K8 Modernization	5	12/19/20	12/22/20											
Owner Move-in - Bldgs B	Cubberley K8 Modernization	5	12/20/20	12/23/20											
Construction - Phs. 4 (Bldg D)	Cubberley K8 Modernization	5	12/24/20	7/9/21											
Owner Move-in Bldg C	Cubberley K8 Modernization	5	2/27/21	2/27/21											
Owner Move-in - Bldg D	Cubberley K8 Modernization	5	7/12/21	7/16/21											
<b>Project Name: Fremont ES HVAC</b>			<b>3/23/20</b>	<b>6/28/21</b>											
Construction - Electrical Upgrades	Fremont ES HVAC	5	3/23/20	6/12/20											
Construction - HVAC	Fremont ES HVAC	5	6/15/20	6/16/21											
Owner Move-in - Ph 1 (AUD/Cafeteria & Portables)	Fremont ES HVAC	5	9/8/20	9/8/20											
Owner Move-in - Ph 2 (Bldgs 1000 & 4000)	Fremont ES HVAC	5	12/21/20	12/21/20											
Owner Move-in - Ph 3 (Bldg 2000)	Fremont ES HVAC	5	6/21/21	6/28/21											
<b>Project Name: Prisk ES Modernization</b>			<b>4/29/20</b>	<b>8/6/21</b>											
Construction - Bldg D	Prisk ES Modernization	5	4/29/20	8/21/20											
Construction - Bldg B	Prisk ES Modernization	5	6/2/20	11/20/20											
Owner Move-in - Bldg D	Prisk ES Modernization	5	8/20/20	8/27/20											
Construction - Bldg C	Prisk ES Modernization	5	11/23/20	3/16/21											
Owner Move-in - Bldg B	Prisk ES Modernization	5	11/23/20	11/25/20											
Owner Move-in - Bldg C	Prisk ES Modernization	5	3/17/21	3/19/21											
Construction - Bldg A	Prisk ES Modernization	5	3/22/21	7/30/21											
Owner Move-in - Bldg A	Prisk ES Modernization	5	8/2/21	8/6/21											

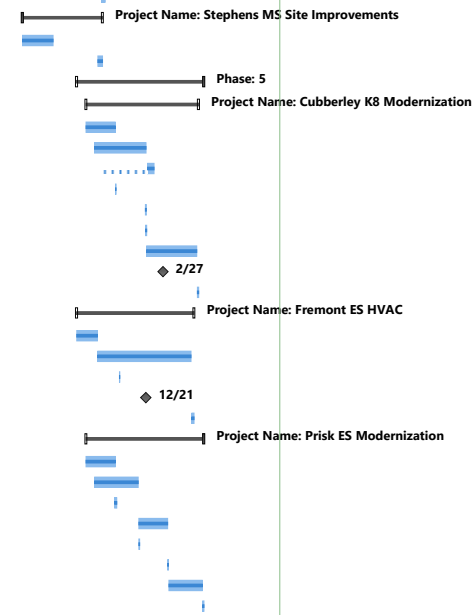

Project updates  
Date: 6/3/22

Task  Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.
