



# I. Major Projects Update

## Jordan High School Major Renovation

### Project Summary:

- Existing facilities built in 1930's and 1940's with additions built in the 1950's through 1990's
- 26.89 acre site
- Existing 301,663 s.f. of permanent and 31,680 s.f. of portable structures
- New and renovated facilities: 395,000 s.f.
- 132 classrooms, six (6) Academies
- Master Plan capacity: 3,600 students

### Project Status:

- Ph. 1A Interim Housing: DSA closeout: Underway
- Construction Documents: Ph. 2B Underway
- Schematic Design complete: 2A, 5, 6
- Phase 1B Demolition: Completed
- Phase 1C DSA approval: Completed
- Design Development 2A: Completed
- Ph. 1B Increment 2: Under construction
- Construction Documents 2A: Underway

### Upcoming Activities:

- DSA Submittal 2A: October 2015



NTD


### Project Team:

- Architect: PJHM
- Contractors:
  - Phase 1A: McCarthy Building Companies
  - Phase 1B Demo: Unlimited Environmental
  - Phase 1B inc.1: Hayward Baker Inc.
  - Phase 1B inc.2: Pinner Construction Company, Inc.



# I. Major Projects Update

## Jordan High School Major Renovation

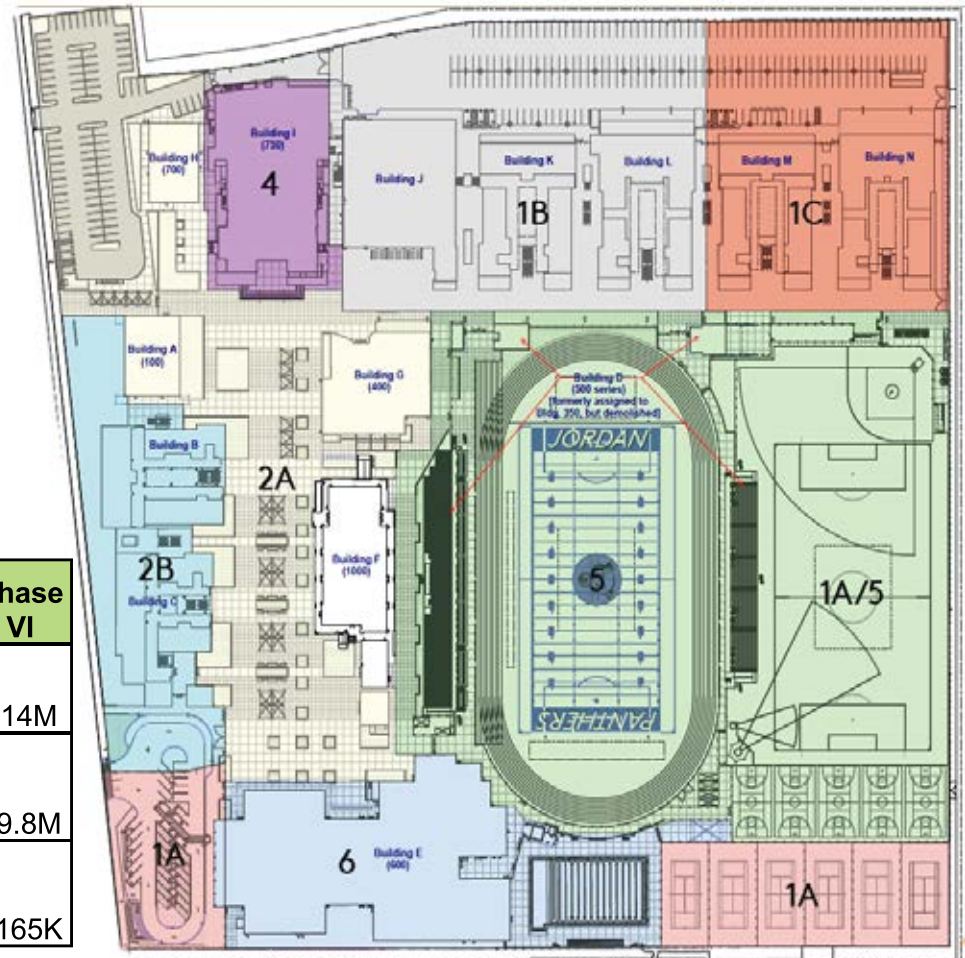

### Budgets:

	Phase I	Phase II	Phase IV*	Phase V	Phase VI
<b>Estimated Total Project Budget</b>	\$104.5 M	\$42.6M	\$20.1M	\$18.3M	\$14M
<b>Estimated Construction Budget</b>	\$74.1M	\$31.7M	\$13.6M	\$14.8M	\$9.8M
<b>Dollars Expended (8/31/15)</b>	\$35.1M	\$380K	\$881K	\$126K	\$165K

\*AB 300 project



# I. Major Projects Update

## Jordan High School Major Renovation

