



I. Major Projects Update

Jordan High School Major Renovation

Project Summary:

- Existing facilities built in 1930's and 1940's with additions built in the 1950's through 1990's
- 26.89 acre site
- Existing 301,663 s.f. of permanent and 31,680 s.f. of portable structures
- New and renovated facilities: 395,000 s.f.
- 132 classrooms, six (6) Academies
- Master Plan capacity: 3,600 students

Project Status:

- Ph. 1A Interim Housing: Completed
- Construction Documents: Ph. 2B Underway
- Schematic Design: 5 and 6 Underway
- Schematic Design complete: 2A and AB 300
- Phase 1B Demolition: Underway
- Phase 1C DSA approval: Completed

Upcoming Activities:

- Design Development 2A: Underway
- Design Development AB 300: Completed
- Ph. 1B Increment 2: procurement underway



Project Team:

- Architect: NTD (Ph. 1, 2B), and PJHM (Ph. 2A, 4, 5, 6)
- Contractors:
 - Phase 1A: McCarthy Building Companies
 - Phase 1B Demo: Unlimited Environmental
 - Phase 1B inc.1: Hayward Baker
 - Phase 1B inc.2: TBD




I. Major Projects Update

Jordan High School Major Renovation

Budgets:

	Phase I	Phase II	Phase IV*	Phase V	Phase VI
Estimated Total Project Budget	\$104M	\$42.6M	\$20.1M	\$18.3M	\$14M
Estimated Construction Budget	\$74M	\$31.7M	\$13.5M	\$14.8M	\$9.8M
Dollars Expended (8/25/14)	\$18.9M	\$202K	\$439K	\$126K	\$151K

*AB 300 project

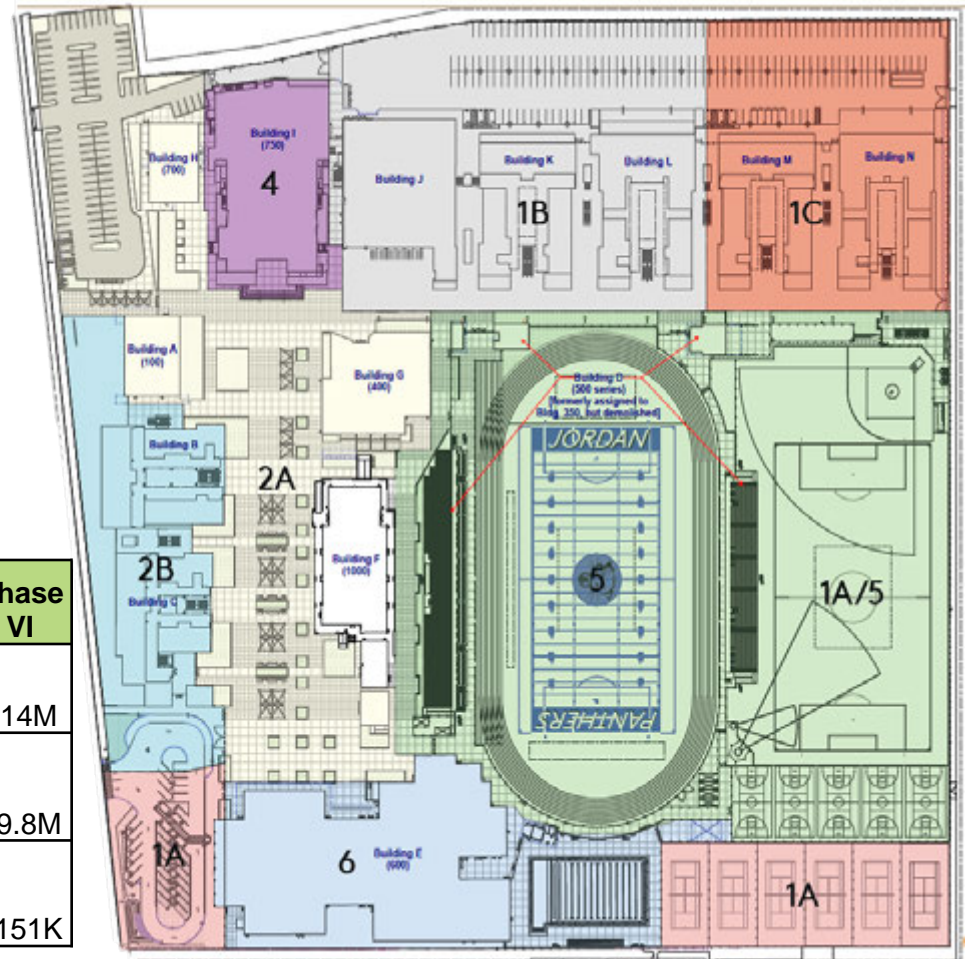



I. Major Projects Update

Jordan High School Major Renovation



Demolition of building 990 footing for site grading preparations.



Crushing concrete to extract the steel rebar, preparation for recycling concrete and metal rebar.



Site Clearing and start of Grading operations for Soil Improvement.



Site Cleared and start of site grading for Phase 1B.
