



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
State: Active			2/5/18	9/21/23											
Phase: 0A			3/4/21	8/31/21											
Project Name: AV Portables Phase III			3/4/21	8/31/21											
Construction	AV Portables Phase III	0A	3/4/21	8/31/21											
Phase: 0EV			8/25/21	8/31/22											
Project Name: EVSS Phase II			8/25/21	8/31/22											
Construction	EVSS Phase II	0EV	8/25/21	8/31/22											
Phase: 0FA			3/10/20	6/30/21											
Project Name: Fire Alarms/Life Safety Sys - Phase V			3/10/20	6/30/21											
Construction	Fire Alarms/Life Safety Sys - Phase V	0FA	3/10/20	6/30/21											
Phase: 0ICS			10/8/20	5/7/21											
Project Name: ICS Phase II			2/4/21	5/7/21											
Construction	ICS Phase II	0ICS	2/4/21	5/7/21											
Project Name: Jordan HS ICS			10/8/20	3/31/21											
Construction	Jordan HS ICS	0ICS	10/8/20	3/31/21											
Phase: 0TC			7/1/21	6/28/23											
Project Name: Telecom Phase II			7/1/21	6/28/23											
Construction	Telecom Phase II	0TC	7/1/21	6/28/23											
Phase: 2			2/5/18	8/13/21											
Project Name: Kettering ES HVAC			2/5/18	8/13/21											
Construction - Classroom Buildings	Kettering ES HVAC	2	2/5/18	8/14/18											
Owner Move-in - Phase 1	Kettering ES HVAC	2	6/16/18	6/22/18											
Construction - Site Work	Kettering ES HVAC	2	8/15/18	11/14/18											
Owner Move-in - Phase 2	Kettering ES HVAC	2	8/18/18	8/30/18											
Construction - Security Fencing & Water Heater Enclosures	Kettering ES HVAC	2	3/1/19	12/30/20											
Construction - Fire Sprinklers	Kettering ES HVAC	2	6/8/21	8/13/21											
Phase: 3			6/25/18	8/16/21											
Project Name: Lakewood HS HVAC			6/25/18	6/30/21											
Construction - Bldg 200	Lakewood HS HVAC	3	6/25/18	11/16/18											
Owner Move-in - Bldg 200	Lakewood HS HVAC	3	11/17/18	11/21/18											
Construction - Bldgs 300 & 900	Lakewood HS HVAC	3	11/26/18	6/21/19											
Owner Move-in - Bldg 300	Lakewood HS HVAC	3	4/22/19	4/25/19											
Construction - Bldgs 100 & 800 (1st & 3rd floors), Cafeteria	Lakewood HS HVAC	3	6/17/19	8/9/19											
Owner Move-in - Bldg 900	Lakewood HS HVAC	3	6/27/19	6/28/19											
Construction - Bldgs 400 & 800	Lakewood HS HVAC	3	8/5/19	12/31/19											
Owner Move-in - Bldg 100 & Cafeteria	Lakewood HS HVAC	3	8/12/19	8/14/19											
Construction - Bldgs 500 & 800 (2nd & 4th floors)	Lakewood HS HVAC	3	8/16/19	12/20/19											
Construction - Bldg 700	Lakewood HS HVAC	3	9/30/19	2/11/20											
Owner Move-in - 400 & 800 (2ns & 4th floors)	Lakewood HS HVAC	3	12/20/19	1/3/20											
Owner Move-in - Bldgs 500 & 700	Lakewood HS HVAC	3	2/10/20	2/14/20											
Construction - Fire Alarm Upgrads (Gyn, Bleachers, Portables, Bungalows)	Lakewood HS HVAC	3	10/19/20	6/30/21											
Project Name: Lowell ES HVAC			9/10/18	8/16/21											
Construction	Lowell ES HVAC	3	9/10/18	8/25/19											
Owner Move-in (Classrooms building)	Lowell ES HVAC	3	6/14/19	6/20/19											
Construction - Aud/Cafeteria Bldgs	Lowell ES HVAC	3	6/17/19	11/27/19											
Owner Move-in (Non-Classrooms)	Lowell ES HVAC	3	8/21/19	8/25/19											
Owner Move-in Aud/Cafeteria Bldgs	Lowell ES HVAC	3	11/28/19	12/4/19											
Construction - Stage Lift	Lowell ES HVAC	3	6/15/21	8/16/21											
Project Name: Mann ES HVAC			9/4/18	8/19/19											
Construction	Mann ES HVAC	3	9/4/18	8/18/19											
Owner Move-in - Phase 1	Mann ES HVAC	3	4/19/19	4/24/19											
Owner Move-in - Phase 2	Mann ES HVAC	3	8/17/19	8/19/19											
Phase: 4			11/18/19	8/24/23											
Project Name: Jordan HS Ph 2B & 3 (Bldgs 2			7/26/21	7/5/23											
Construction - 2B (Bldg 200)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	7/26/21	5/5/23											
Construction - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	9/26/22	5/22/23											
Owner Move-in - 3 (Bldg 1000)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	5/23/23	6/1/23											
Owner Move-in - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3 (Bldgs 200/300/1000)	4	6/26/23	7/5/23											

Project updates
Date: 6/7/21

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: Rogers MS Portables					Project Name: Rogers MS Portables										
Construction	Rogers MS Portables	4	6/17/20	8/24/23											
Owner Move-in	Rogers MS Portables	4	9/7/20	9/11/20											
Construction - Demo Russel Bungalows	Rogers MS Portables	4	6/21/22	8/24/23											
Project Name: Stevenson ES Auditorium Rep.					Project Name: Stevenson ES Auditorium Repairs										
Construction - Auditorium	Stevenson ES Auditorium Repairs	4	11/18/19	6/10/20											
Construction - Campuse-wide Fire Alarm Upgrade	Stevenson ES Auditorium Repairs	4	11/18/19	8/21/20											
Construction - Cafeteria/Kitchen	Stevenson ES Auditorium Repairs	4	6/11/20	10/30/20											
Owner Move-in	Stevenson ES Auditorium Repairs	4	8/23/20	8/27/20											
Phase: 5					Phase: 5										
Project Name: Cubberley K8 Modernization					Project Name: Cubberley K8 Modernization										
Construction - Ph. 1 (Bldg E)	Cubberley K8 Modernization	5	4/29/20	8/21/20											
Construction - Ph. 2 (Bldgs A & B)	Cubberley K8 Modernization	5	6/1/20	12/21/20											
Construction - Ph. 3 (Bldg C)	Cubberley K8 Modernization	5	6/22/20	1/21/21											
Owner Move-in - Bldg E	Cubberley K8 Modernization	5	8/24/20	8/24/20											
Owner Move-in Bldg A	Cubberley K8 Modernization	5	12/19/20	12/22/20											
Owner Move-in - Bldgs B	Cubberley K8 Modernization	5	12/20/20	12/23/20											
Construction - Phs. 4 (Bldg D)	Cubberley K8 Modernization	5	12/24/20	7/9/21											
Owner Move-in Bldg C	Cubberley K8 Modernization	5	2/27/21	2/27/21											
Owner Move-in - Bldg D	Cubberley K8 Modernization	5	7/12/21	7/16/21											
Project Name: Fremont ES HVAC					Project Name: Fremont ES HVAC										
Construction - Electrical Upgrades	Fremont ES HVAC	5	3/23/20	6/12/20											
Construction - HVAC	Fremont ES HVAC	5	6/15/20	6/16/21											
Owner Move-in - Ph 1 (AUD/Cafeteria & Portables)	Fremont ES HVAC	5	9/8/20	9/8/20											
Owner Move-in - Ph 2 (Bldgs 1000 & 4000)	Fremont ES HVAC	5	12/21/20	12/21/20											
Owner Move-in - Ph 3 (Bldg 2000)	Fremont ES HVAC	5	6/21/21	6/28/21											
Project Name: Lakewood HS Track/Field					Project Name: Lakewood HS Track/Field										
Construction	Lakewood HS Track/Field	5	2/24/21	8/26/21											
Owner Move-in	Lakewood HS Track/Field	5	8/23/21	8/26/21											
Project Name: Madison ES HVAC					Project Name: Madison ES HVAC										
Construction - Phase 1	Madison ES HVAC	5	7/9/20	1/22/21											
Owner Move-in - Phase 1	Madison ES HVAC	5	1/25/21	1/26/21											
Construction - Phase 2	Madison ES HVAC	5	2/1/21	8/18/21											
Owner Move-in - Phase 2	Madison ES HVAC	5	8/19/21	8/24/21											
Project Name: Prisk ES Modernization					Project Name: Prisk ES Modernization										
Construction - Bldg D	Prisk ES Modernization	5	4/29/20	8/21/20											
Construction - Bldg B	Prisk ES Modernization	5	6/2/20	11/20/20											
Owner Move-in - Bldg D	Prisk ES Modernization	5	8/20/20	8/27/20											
Construction - Bldg C	Prisk ES Modernization	5	11/23/20	3/16/21											
Owner Move-in - Bldg B	Prisk ES Modernization	5	11/23/20	11/25/20											
Owner Move-in - Bldg C	Prisk ES Modernization	5	3/17/21	3/19/21											
Construction - Bldg A	Prisk ES Modernization	5	3/22/21	7/30/21											
Owner Move-in - Bldg A	Prisk ES Modernization	5	8/2/21	8/6/21											
Project Name: Wilson HS HVAC					Project Name: Wilson HS HVAC										
Construction Phase 1 (Bldg 100 North)	Wilson HS HVAC	5	6/15/20	11/20/20											
Construction Phase 2 (Bldg 100 East)	Wilson HS HVAC	5	10/2/20	3/12/21											
Owner Move-in Phase 1 (Bldg 100 North)	Wilson HS HVAC	5	1/4/21	1/6/21											
Construction Phase 3 (Bldg 100 West)	Wilson HS HVAC	5	2/2/21	6/28/21											
Owner Move-in - Phase 2 (Bldg 100 East)	Wilson HS HVAC	5	3/12/21	3/12/21											
Construction Phase 4 (Bldg 200)	Wilson HS HVAC	5	6/18/21	11/4/21											
Owner Move-in Phase 3 (Bldg 100 West)	Wilson HS HVAC	5	6/29/21	7/1/21											
Owner Move-in Phase 4 (Bldg 200)	Wilson HS HVAC	5	10/29/21	11/4/21											
Construction Phase 5 (Bldg 300)	Wilson HS HVAC	5	11/5/21	3/23/22											
Owner Move-in Phase 5 (Bldg 300)	Wilson HS HVAC	5	3/17/22	3/23/22											
Construction Phase 6 (Bldg 400)	Wilson HS HVAC	5	3/24/22	8/18/22											
Construction Phase 7 (Room 510 and Portables)	Wilson HS HVAC	5	6/15/22	8/8/22											
Owner Move-in Phase 7 (Room 510 and Portables)	Wilson HS HVAC	5	8/9/22	8/15/22											
Owner Move-in Phase 6 (Bldg 400)	Wilson HS HVAC	5	8/19/22	8/25/22											
Phase: 6					Phase: 6										

Project updates
Date: 6/7/21

Task Summary



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: Bryant ES Modernization					Project Name: Bryant ES Modernization										
Construction	Bryant ES Modernization	6	6/15/21	2/10/22											
Owner Move-in	Bryant ES Modernization	6	1/13/22	2/10/22											
Project Name: Hughes MS HVAC					Project Name: Hughes MS HVAC										
Construction - Elect. Upgrades	Hughes MS HVAC	6	6/19/20	7/11/22											
Construction - Kitchen and Cafeteria, and Auditorium	Hughes MS HVAC	6	4/5/21	8/13/21											
Construction - Bldgs 200/300/600/700 & existing portables	Hughes MS HVAC	6	6/29/21	12/20/21											
Owner Move-in - Kitchen and Cafeteria, and Auditorium	Hughes MS HVAC	6	8/16/21	8/30/21											
Owner Move-in - Bldgs 200/300/600/700 & existing portable	Hughes MS HVAC	6	12/21/21	12/31/21											
Construction - Bldgs 100/400/800/900	Hughes MS HVAC	6	12/27/21	7/4/22											
Owner Move-in - Idgs 100/400/800/900	Hughes MS HVAC	6	7/5/22	7/11/22											
Project Name: Lakewood HS Gym					Project Name: Lakewood HS Gym										
Construction	Lakewood HS Gym	6	1/15/22	8/22/22											
Owner Move-in	Lakewood HS Gym	6	8/23/22	8/26/22											
Project Name: Lowell ES Portables					Project Name: Lowell ES Portables										
Construction	Lowell ES Portables	6	6/18/21	8/27/21											
Owner Move-in	Lowell ES Portables	6	8/27/21	8/27/21											
Project Name: Robinson K8 HVAC					Project Name: Robinson K8 HVAC										
Construction	Robinson K8 HVAC	6	8/2/21	8/15/22											
Owner Move-in	Robinson K8 HVAC	6	8/2/22	8/15/22											
Project Name: Twain ES HVAC					Project Name: Twain ES HVAC										
Construction - HVAC Phase 1	Twain ES HVAC	6	6/21/21	8/29/22											
Owner Move-in - Phase 1	Twain ES HVAC	6	12/26/21	1/5/22											
Construction - HVAC Phase 2	Twain ES HVAC	6	1/6/22	6/20/22											
Owner Move-in - Phase 2	Twain ES HVAC	6	6/21/22	7/4/22											
Construction - Caf� & Kitchen Phase 3	Twain ES HVAC	6	6/22/22	8/24/22											
Owner Move-in Phase 3	Twain ES HVAC	6	8/25/22	8/29/22											
Phase: 7					Phase: 7										
Project Name: Avalon K-12 HVAC					Project Name: Avalon K-12 HVAC										
Construction Phase 1 - Bldg G	Avalon K-12 HVAC	7	12/31/21	6/15/22											
Owner Move-in Phase 1 Bldg G	Avalon K-12 HVAC	7	6/16/22	6/29/22											
Construction Phase 2 - Bldgs E & F	Avalon K-12 HVAC	7	6/30/22	8/17/22											
Construction Phase 3 - Bldg A	Avalon K-12 HVAC	7	6/30/22	12/14/22											
Owner Move-in Phase 2 Bldgs E & F	Avalon K-12 HVAC	7	8/18/22	8/24/22											
Owner Move-in Phase 3 Bldg A	Avalon K-12 HVAC	7	12/15/22	12/29/22											
Construction Phase 4 - Bldgs B & D	Avalon K-12 HVAC	7	12/30/22	6/14/23											
Construction Phase 5A - Bldg C	Avalon K-12 HVAC	7	4/17/23	8/18/23											
Owner Move-in Phase 4 Bldgs B & D	Avalon K-12 HVAC	7	6/15/23	6/28/23											
Construction Phase 5B - Portables	Avalon K-12 HVAC	7	7/3/23	8/18/23											
Owner Move-in Phase 5A & B Bldg C	Avalon K-12 HVAC	7	8/21/23	8/25/23											
Project Name: Bancroft MS HVAC					Project Name: Bancroft MS HVAC										
Construction	Bancroft MS HVAC	7	4/20/22	8/31/23											
Owner Move-in	Bancroft MS HVAC	7	8/29/23	8/31/23											
Project Name: Hamilton MS Gym Measure K					Project Name: Hamilton MS Gym Measure K										
Construction	Hamilton MS Gym Measure K	7	6/17/22	9/11/23											
Owner Move-in	Hamilton MS Gym Measure K	7	9/12/23	9/21/23											
Project Name: Holmes ES HVAC					Project Name: Holmes ES HVAC										
Construction - Phase 1	Holmes ES HVAC	7	6/20/22	12/16/22											
Owner Move-in - Phase 1	Holmes ES HVAC	7	12/26/22	1/6/23											
Construction - Phase 2	Holmes ES HVAC	7	1/9/23	6/15/23											
Owner Move-in - Phase 2	Holmes ES HVAC	7	6/23/23	7/5/23											
Project Name: Keller MS New Locker Room					Project Name: Keller MS New Locker Room										
Construction	Keller MS New Locker Room	7	6/13/22	6/23/23											
Owner Move-in	Keller MS New Locker Room	7	6/12/23	6/23/23											
Project Name: Wilson HS Aquatic Center					Project Name: Wilson HS Aquatic Center										
Construction	Wilson HS Aquatic Center	7	9/1/22	9/12/23											
Owner Move-in	Wilson HS Aquatic Center	7	9/13/23	9/19/23											
State: Complete					State: Complete										
Phase: 0A					Phase: 0A										

Project updates
Date: 6/7/21

Task Summary



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: AV Portables Phase I			8/1/19	3/27/20											
Construction	AV Portables Phase I	OA	8/1/19	3/27/20											
Project Name: AV Portables Phase II			6/15/20	8/21/20											
Construction	AV Portables Phase II	OA	6/15/20	8/21/20											
Phase: OFA			6/30/16	1/31/20											
Project Name: Fire Alarms/Life Safety Sys - Phase II			6/30/16	6/30/17											
Construction	Fire Alarms/Life Safety Sys - Phase II	OFA	6/30/16	6/30/17											
Project Name: Fire Alarms/Life Safety Sys - Phase III			7/20/17	9/14/18											
Construction - Monroe	Fire Alarms/Life Safety Sys - Phase III	OFA	7/20/17	12/31/17											
Construction - Marshall	Fire Alarms/Life Safety Sys - Phase III	OFA	9/1/17	9/14/18											
Construction - Cubberly/King	Fire Alarms/Life Safety Sys - Phase III	OFA	9/1/17	9/14/18											
Project Name: Fire Alarms/Life Safety Sys - Phase IV			12/10/18	1/31/20											
Construction	Fire Alarms/Life Safety Sys - Phase IV	OFA	12/10/18	1/31/20											
Phase: OICS			8/1/16	10/15/20											
Project Name: ICS			8/1/16	10/15/20											
Construction	ICS	OICS	8/1/16	10/15/20											
Phase: OS			8/22/18	2/28/20											
Project Name: Security Improvements			8/22/18	2/28/20											
Construction	Security Improvements	OS	8/22/18	2/28/20											
Phase: OSC			7/6/17	1/30/18											
Project Name: Security Camera Phase II			7/6/17	1/30/18											
Construction	Security Camera Phase II	OSC	7/6/17	1/30/18											
Phase: OW			9/22/17	8/31/18											
Project Name: E Rate 2016 / 2017			9/22/17	8/31/18											
Construction	E Rate 2016 / 2017	OW	9/22/17	8/31/18											
Project Name: Wireless Phase V			1/4/18	4/4/18											
Construction	Wireless Phase V	OW	1/4/18	4/4/18											
Phase: 1			10/1/14	1/29/21											
Project Name: Barton/Educare ES			2/24/17	7/3/18											
Construction	Barton/Educare ES	1	2/24/17	5/17/18											
Owner Move-in	Barton/Educare ES	1	7/2/18	7/3/18											
Project Name: Browning HS New Construction			10/1/14	5/28/19											
Construction	Browning HS New Construction	1	10/1/14	12/28/17											
Owner Move-in	Browning HS New Construction	1	7/31/17	1/11/18											
Additional Construction - Site and off-site Work	Browning HS New Construction	1	12/29/17	5/28/19											
Project Name: Cabrillo HS Track/Field			6/15/17	11/28/17											
Construction	Cabrillo HS Track/Field	1	6/15/17	10/26/17											
Owner Move-in	Cabrillo HS Track/Field	1	11/14/17	11/28/17											
Project Name: Head Start at Bethune			3/8/18	5/14/18											
Construction	Head Start at Bethune	1	3/8/18	5/4/18											
Owner Move-in	Head Start at Bethune	1	5/8/18	5/14/18											
Project Name: Head Start at Hudson			10/23/17	4/12/18											
Construction	Head Start at Hudson	1	10/23/17	4/11/18											
Owner Move-in	Head Start at Hudson	1	4/12/18	4/12/18											
Project Name: Head Start at Jordan Plus			10/24/17	5/8/18											
Construction	Head Start at Jordan Plus	1	10/24/17	5/7/18											
Owner Move-in	Head Start at Jordan Plus	1	5/8/18	5/8/18											
Project Name: Jordan HS Ph 1C, 1D & 4			10/18/17	1/29/21											
Construction - Phase 1C & 1D	Jordan HS Ph 1C, 1D & 4	1	10/18/17	12/20/19											
Construction - Phase 4	Jordan HS Ph 1C, 1D & 4	1	10/18/17	1/29/21											
Owner Move-in Phase 1C (Bldgs 1400 & 1500)	Jordan HS Ph 1C, 1D & 4	1	12/21/19	1/3/20											
Owner Move-in Phase 4	Jordan HS Ph 1C, 1D & 4	1	12/1/20	12/1/20											
Project Name: Kettering ES Interim Housing			10/19/17	2/20/18											
Construction	Kettering ES Interim Housing	1	10/19/17	2/20/18											
Owner Move-in	Kettering ES Interim Housing	1	12/16/17	1/3/18											
Project Name: Monroe K8 Interim Housing			7/21/17	12/26/17											
Construction	Monroe K8 Interim Housing	1	7/21/17	12/11/17											
Owner Move-in	Monroe K8 Interim Housing	1	12/22/17	12/26/17											

Project updates
Date: 6/7/21

Task Summary



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: Poly HS ADA Improvements			6/19/17	9/28/18											
Construction	Poly HS ADA Improvements	1	6/19/17	9/28/18											
Project Name: Poly HS Auditorium			1/6/15	11/2/17											
Construction	Poly HS Auditorium	1	1/6/15	10/26/17											
Owner Move-in	Poly HS Auditorium	1	10/23/17	11/2/17											
Project Name: Poly HS Band Bldg Conversio			10/23/17	11/16/17											
Construction	Poly HS Band Bldg Conversion Work	1	10/23/17	11/14/17											
Owner Move-in	Poly HS Band Bldg Conversion Work	1	11/15/17	11/16/17											
Project Name: Renaissance HS			9/6/16	1/4/19											
Construction	Renaissance HS	1	9/6/16	1/4/19											
Owner Move-in	Renaissance HS	1	7/16/18	7/16/18											
Project Name: Riley ES Interim Housing			10/20/17	12/28/17											
Construction	Riley ES Interim Housing	1	10/20/17	12/22/17											
Owner Move-in	Riley ES Interim Housing	1	12/27/17	12/28/17											
Project Name: Rogers MS Interim Housing			10/16/17	12/31/17											
Construction	Rogers MS Interim Housing	1	10/16/17	12/7/17											
Owner Move-in	Rogers MS Interim Housing	1	12/29/17	12/31/17											
Project Name: Sato HS Conversion			6/5/17	9/8/17											
Construction	Sato HS Conversion	1	6/5/17	9/8/17											
Owner Move-in	Sato HS Conversion	1	8/1/17	8/18/17											
Project Name: Sato HS Gym			5/23/16	1/31/18											
Construction	Sato HS Gym	1	5/23/16	1/31/18											
Owner Move-in	Sato HS Gym	1	8/21/17	1/8/18											
Project Name: Wilson HS Auditorium			2/22/16	3/6/18											
Construction	Wilson HS Auditorium	1	2/22/16	2/19/18											
Owner Move-in	Wilson HS Auditorium	1	2/21/18	3/6/18											
Project Name: Wilson HS Track/Field			9/18/17	4/9/18											
Construction	Wilson HS Track/Field	1	9/18/17	3/30/18											
Owner Move-in	Wilson HS Track/Field	1	4/3/18	4/9/18											
Phase: 2			12/20/17	9/4/20											
Project Name: Cleveland ES HVAC			1/3/18	8/23/18											
Construction	Cleveland ES HVAC	2	1/3/18	8/13/18											
Owner Move-in	Cleveland ES HVAC	2	8/21/18	8/23/18											
Project Name: Garfield ES HVAC			2/6/18	11/16/18											
Construction - Phase 1 (Site, Bldgs C & E)	Garfield ES HVAC	2	2/6/18	7/13/18											
Construction - Phase 2 (Bldgs A, D, & F)	Garfield ES HVAC	2	7/16/18	8/24/18											
Owner Move-In - Phase 1	Garfield ES HVAC	2	8/13/18	8/18/18											
Owner Move-in - Phase 2	Garfield ES HVAC	2	8/20/18	8/28/18											
Construction - Phase 3	Garfield ES HVAC	2	8/27/18	11/16/18											
Owner Move-in - Phase 3	Garfield ES HVAC	2	10/20/18	10/20/18											
Project Name: Poly HS Track/Field			12/20/17	9/10/18											
Construction	Poly HS Track/Field	2	12/20/17	9/10/18											
Owner Move-in	Poly HS Track/Field	2	9/10/18	9/10/18											
Project Name: Riley ES HVAC			1/3/18	12/23/18											
Construction - Classroom Building	Riley ES HVAC	2	1/3/18	8/10/18											
Construction - Site Work	Riley ES HVAC	2	8/11/18	12/23/18											
Owner Move-in	Riley ES HVAC	2	8/14/18	8/20/18											
Project Name: Rogers MS HVAC			2/12/18	9/4/20											
Construction	Rogers MS HVAC	2	2/12/18	8/14/18											
Owner Move-in	Rogers MS HVAC	2	8/15/18	8/27/18											
Construction - Locker Room	Rogers MS HVAC	2	6/20/20	9/4/20											
Project Name: Rogers MS Track/Field			6/18/18	8/27/18											
Construction	Rogers MS Track/Field	2	6/18/18	8/24/18											
Owner Move-in	Rogers MS Track/Field	2	8/27/18	8/27/18											
Project Name: Stephens MS HVAC			2/9/18	8/30/18											
Construction	Stephens MS HVAC	2	2/9/18	8/17/18											
Owner Move-in (furniture)	Stephens MS HVAC	2	7/23/18	8/30/18											
Owner Move-in - final	Stephens MS HVAC	2	8/13/18	8/18/18											


Project updates
Date: 6/7/21

Task Summary



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: Stephens MS Track/Field			4/16/18	9/18/18											
Construction	Stephens MS Track/Field	2	4/16/18	9/17/18											
Owner Move-in	Stephens MS Track/Field	2	9/18/18	9/18/18											
Project Name: Webster ES Interim Housing			1/3/18	8/11/18											
Construction	Webster ES Interim Housing	2	1/3/18	7/30/18											
Owner Move-in	Webster ES Interim Housing	2	7/31/18	8/11/18											
Phase: 3			6/11/18	10/14/20											
Project Name: Barton ES HVAC			6/18/18	8/25/19											
Construction - Phase 1	Barton ES HVAC	3	6/18/18	12/21/18											
Owner Move-in Phase 1	Barton ES HVAC	3	12/31/18	1/2/19											
Construction - Phase 2	Barton ES HVAC	3	1/3/19	6/19/19											
Owner Move-in Phase 2	Barton ES HVAC	3	6/19/19	6/21/19											
Construction - Phase 3	Barton ES HVAC	3	6/22/19	8/20/19											
Owner Move-in Phase 3	Barton ES HVAC	3	8/21/19	8/25/19											
Project Name: Burcham ES HVAC			6/25/18	9/25/19											
Construction	Burcham ES HVAC	3	6/25/18	9/25/19											
Owner Move-in - Phase 1	Burcham ES HVAC	3	1/2/19	1/18/19											
Owner Move-in - Phase 2	Burcham ES HVAC	3	7/29/19	7/31/19											
Owner Move-in - Phase 3	Burcham ES HVAC	3	8/26/19	8/26/19											
Project Name: Jefferson MS HVAC			9/10/18	6/30/20											
Construction	Jefferson MS HVAC	3	9/10/18	8/26/19											
Construction - elevator	Jefferson MS HVAC	3	5/1/19	6/30/20											
Owner Move-in	Jefferson MS HVAC	3	8/22/19	8/26/19											
Project Name: Jefferson MS Track/Field			12/1/18	8/25/19											
Construction	Jefferson MS Track/Field	3	12/1/18	8/25/19											
Owner Move-in	Jefferson MS Track/Field	3	8/21/19	8/25/19											
Project Name: Jordan HS Ph 2A (Bldgs 100/400)			10/25/18	10/14/20											
Construction	Jordan HS Ph 2A (Bldgs 100/400)	3	10/25/18	9/30/20											
Owner Move-in (Bldg 100)	Jordan HS Ph 2A (Bldgs 100/400)	3	12/21/19	1/3/20											
Owner Move-in (Bldg 400)	Jordan HS Ph 2A (Bldgs 100/400)	3	10/13/20	10/14/20											
Project Name: Keller MS Conversion			9/12/18	4/26/19											
Construction	Keller MS Conversion	3	9/12/18	4/25/19											
Owner Move-in - Phase 1	Keller MS Conversion	3	4/25/19	4/26/19											
Project Name: Keller MS HVAC			9/12/18	8/20/19											
Construction	Keller MS HVAC	3	9/12/18	8/19/19											
Owner Move-in - Phase 1	Keller MS HVAC	3	4/25/19	4/28/19											
Owner Move-in - Phase 2	Keller MS HVAC	3	8/20/19	8/20/19											
Project Name: Lindsey MS HVAC (Bldg D)			6/18/18	1/2/19											
Construction	Lindsey MS HVAC (Bldg D)	3	6/18/18	12/21/18											
Owner Move-in	Lindsey MS HVAC (Bldg D)	3	1/2/19	1/2/19											
Project Name: Longfellow ES HVAC			6/18/18	8/27/20											
Construction - Auditorium	Longfellow ES HVAC	3	6/18/18	8/11/18											
Construction - CR Bldgs 1000 & 2000	Longfellow ES HVAC	3	7/2/18	4/26/19											
Owner Move-In - Auditorium	Longfellow ES HVAC	3	8/12/18	8/16/18											
Construction - CR Bldgs 3000 & 4000	Longfellow ES HVAC	3	4/22/19	8/13/19											
Construction - Kindergarten Rooms	Longfellow ES HVAC	3	4/22/19	10/29/19											
Owner Move-in - CR Bldgs 1000 & 2000	Longfellow ES HVAC	3	4/24/19	4/28/19											
Owner Move-in - CR Bldgs 3000 & 4000	Longfellow ES HVAC	3	8/14/19	8/18/19											
Owner Move-in - Kindergarten Rooms	Longfellow ES HVAC	3	11/25/19	11/29/19											
Construction - Kitchen	Longfellow ES HVAC	3	6/18/20	8/27/20											
Owner Move-in - Kitchen	Longfellow ES HVAC	3	8/27/20	8/27/20											
Project Name: MacArthur ES HVAC			6/25/18	8/21/19											
Construction - Bldgs B & C	MacArthur ES HVAC	3	6/25/18	1/2/19											
Construction - Bldg A	MacArthur ES HVAC	3	12/24/18	4/19/19											
Owner Move-in Bldgs B & C	MacArthur ES HVAC	3	1/2/19	1/4/19											
Owner Move-in Bldg A	MacArthur ES HVAC	3	4/20/19	4/23/19											
Construction - Bldg D	MacArthur ES HVAC	3	4/24/19	8/16/19											
Construction - Bldg E	MacArthur ES HVAC	3	6/13/19	8/19/19											
Owner Move-in Bldgs D & E	MacArthur ES HVAC	3	8/17/19	8/21/19											

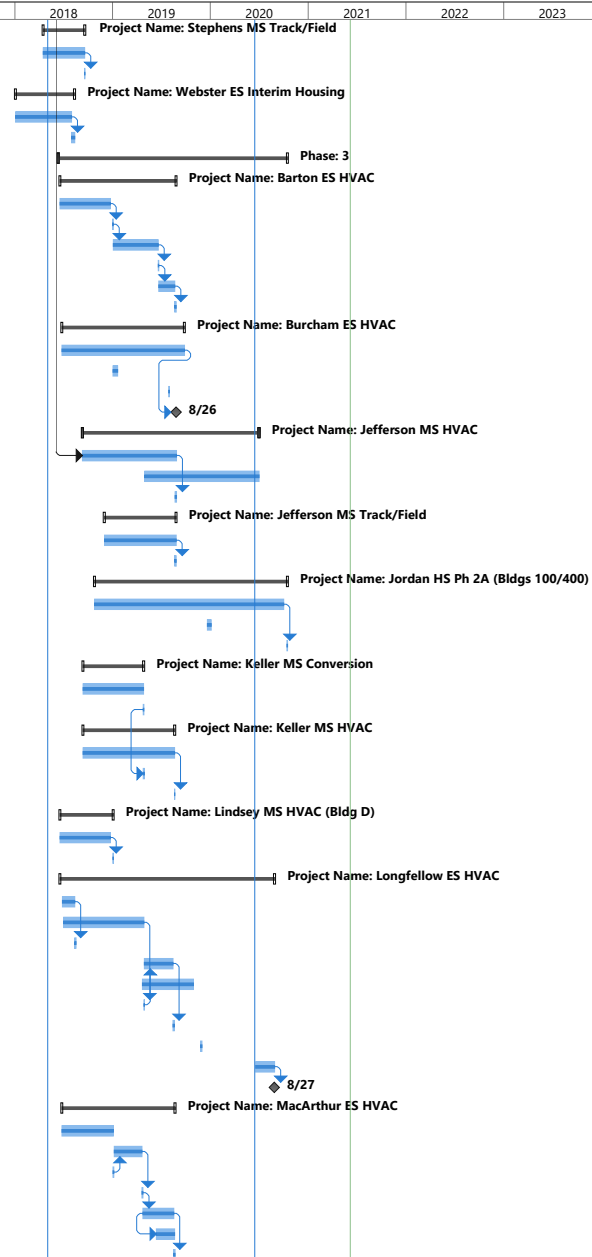

Project updates
Date: 6/7/21

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE (up to Phase 7 projects) as of 5/31/2021

Task Name	Project Name	Phase	Start	Finish	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026
Project Name: McKinley ES HVAC			6/18/18	7/3/19											
Construction Phase 1	McKinley ES HVAC	3	6/18/18	12/21/18											
Owner Move-in Phase 1	McKinley ES HVAC	3	12/26/18	12/27/18											
Construction Phase 2	McKinley ES HVAC	3	12/28/18	7/1/19											
Owner Move-in Phase 2	McKinley ES HVAC	3	7/1/19	7/3/19											
Project Name: Millikan HS New 1000 Bldg			12/3/18	8/28/20											
Construction	Millikan HS New 1000 Bldg	3	12/3/18	8/3/20											
Owner Move-in	Millikan HS New 1000 Bldg	3	8/26/20	8/28/20											
Project Name: Poly HS Bleachers and Field L			12/21/18	9/5/19											
Construction - Soil Remediation	Poly HS Bleachers and Field Lighting	3	12/21/18	1/4/19											
Construction	Poly HS Bleachers and Field Lighting	3	1/22/19	9/5/19											
Project Name: Sato HS New Bldg			6/11/18	8/19/19											
Construction	Sato HS New Bldg	3	6/11/18	8/12/19											
Owner Move-in	Sato HS New Bldg	3	8/13/19	8/19/19											
Project Name: Webster ES HVAC			8/27/18	8/20/19											
Construction - Phase 1	Webster ES HVAC	3	8/27/18	5/31/19											
Construction - Auditorium	Webster ES HVAC	3	4/22/19	8/16/19											
Construction - Cafeteria/Kitchen	Webster ES HVAC	3	6/15/19	8/20/19											
Owner Move-in Phase 1	Webster ES HVAC	3	8/17/19	8/17/19											
Owner Move-in Auditorium/Café/Kitchen	Webster ES HVAC	3	8/17/19	8/18/19											
Phase: 4			6/14/19	11/30/20											
Project Name: Alvarado ES HVAC			7/22/19	7/24/20											
Construction	Alvarado ES HVAC	4	7/22/19	7/10/20											
Owner Move-in	Alvarado ES HVAC	4	7/13/20	7/24/20											
Project Name: Bixby ES HVAC			6/14/19	7/21/20											
Construction	Bixby ES HVAC	4	6/14/19	7/17/20											
Owner Move-in - Phase 1	Bixby ES HVAC	4	8/20/19	8/29/19											
Owner Move-in - Phase 2	Bixby ES HVAC	4	11/25/19	11/27/19											
Owner Move-in - Phase 3	Bixby ES HVAC	4	2/29/20	2/29/20											
Owner Move-in - Phase 4	Bixby ES HVAC	4	7/20/20	7/21/20											
Project Name: Hughes MS Portables			6/20/19	9/2/20											
Construction - AC Paving	Hughes MS Portables	4	6/20/19	8/22/19											
Construction - Portable Installation	Hughes MS Portables	4	4/13/20	4/17/20											
Construction - Electrical and Low Voltage work	Hughes MS Portables	4	6/15/20	9/1/20											
Owner Move-in	Hughes MS Portables	4	9/2/20	9/2/20											
Project Name: Millikan HS Track/Field			1/2/20	11/30/20											
Construction	Millikan HS Track/Field	4	1/2/20	11/27/20											
Owner Move-in	Millikan HS Track/Field	4	11/30/20	11/30/20											
Project Name: Muir K8 HVAC			8/12/19	8/25/20											
Construction - Bldgs B & C	Muir K8 HVAC	4	8/12/19	12/20/19											
Owner Move-in - Bldgs B & C	Muir K8 HVAC	4	12/26/19	12/31/19											
Construction - Bldg A	Muir K8 HVAC	4	1/1/20	7/20/20											
Construction - Bldg D	Muir K8 HVAC	4	5/4/20	8/23/20											
Owner Move-in - Bldg A	Muir K8 HVAC	4	8/12/20	8/14/20											
Owner Move-in - Bldg D	Muir K8 HVAC	4	8/24/20	8/25/20											
Project Name: Naples ES Modernization			10/3/19	7/13/20											
Construction - Bldg 100	Naples ES Modernization	4	10/3/19	5/15/20											
Construction - Bldg 200	Naples ES Modernization	4	10/3/19	5/15/20											
Construction - Bldg 200 Lobby	Naples ES Modernization	4	3/16/20	5/15/20											
Construction - Bldg 300	Naples ES Modernization	4	3/26/20	6/29/20											
Owner Move-in Bldg 100	Naples ES Modernization	4	5/23/20	5/23/20											
Owner Move-in Bldgs 200 and 300	Naples ES Modernization	4	6/30/20	7/13/20											
Project Name: Stephens MS Site Improveme			8/22/19	7/2/20											
Construction	Stephens MS Site Improvements	4	8/22/19	12/20/19											
Owner Move-in	Stephens MS Site Improvements	4	6/15/20	7/2/20											

Project updates
Date: 6/7/21

Task Summary
