



II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

Project Summary:

- Seismic upgrade to auditorium building identified on the State's AB300 report
- Scope of work is limited to seismic upgrade and subject to confirmation with DSA
- Interim housing (portables) during construction

Project Status:

- Construction NTP issued : January 26, 2015
- OPSC Conceptual/Funding Application : Under review
- DSA project approval: Completed July 2, 2014
- Interim Housing: Buildings occupied January 26, 2015
- Board approval of Construction contract: December 9, 2014

Upcoming Activities:

- Construction: Underway
- Contractor mobilization: Complete
- Interior selective demolition: Underway



Project Team:

- Architect: LPA, Inc.
- Contractor Interim Housing: Winter Park Co.
- Contractor: Pinner Construction Company Inc.


Budget:

- Estimated Total Project Budget: \$20.31M
- Estimated Construction Budget: \$14.3M
- Dollars Expended (as of 2/28/15): \$2.26M



II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

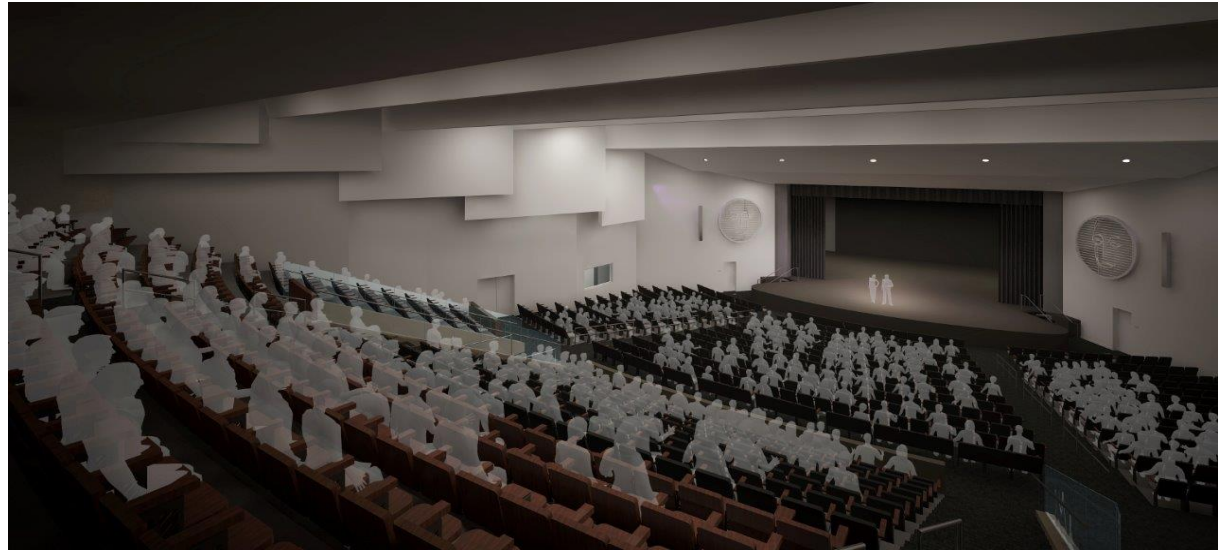

Long Beach Unified School District



II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

