



## II. District-Wide Projects Update

### Polytechnic HS Auditorium AB300

#### Project Summary:

- Seismic upgrade to auditorium building identified on the State's AB300 report
- Scope of work is limited to seismic upgrade and subject to confirmation with DSA
- Interim housing (portables) during construction

#### Project Status:

- Construction anticipated: January 2015
- OPSC Conceptual/Funding Application : Under review
- DSA project approval: Completed July 2, 2014
- Interim Housing: Completion anticipated December 20, 2014
- Board approval of Construction contract: December 9, 2014

#### Upcoming Activities:

- Construction procurement: Underway



#### Project Team:

- Architect: LPA, Inc.
- Contractor Interim Housing: Winter Park Co.
- Contractor: Pinner Construction Company Inc.


#### Budget:

- Estimated Total Project Budget: \$20.31M
- Estimated Construction Budget: \$14M
- Dollars Expended (as of 11/28/14): \$1.83M



## II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

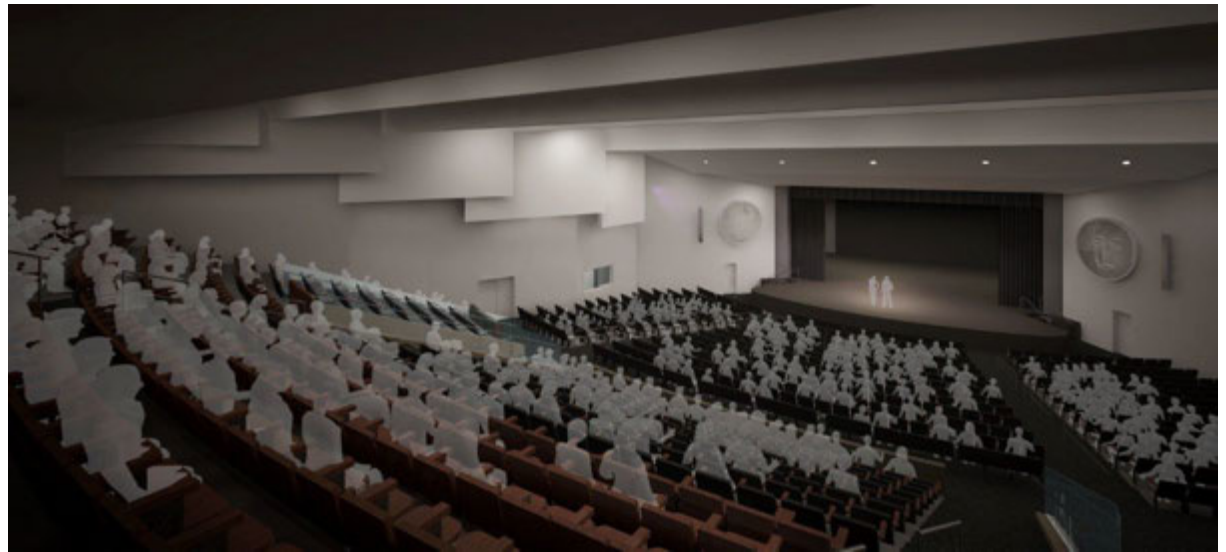

Long Beach Unified School District
