



II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

Project Summary:

- Seismic upgrade to auditorium building identified on the State's AB300 report
- Scope of work is limited to seismic upgrade and subject to confirmation with DSA



Project Status:

- DSA confirmation of SMP Funding eligibility: Phase 4
- Construction Anticipated: Fall 2014
- OPSC Conceptual Submittal: Under review
- CDE Final Approval: Complete

Project Team:

- Architect: LPA, Inc.


Budget:

- Estimated Total Project Budget: \$20.31M
- Estimated Construction Budget: \$14.14M
- Dollars Expended (as of 5/16/14): \$1.46M



II. District-Wide Projects Update

Polytechnic HS Auditorium AB300

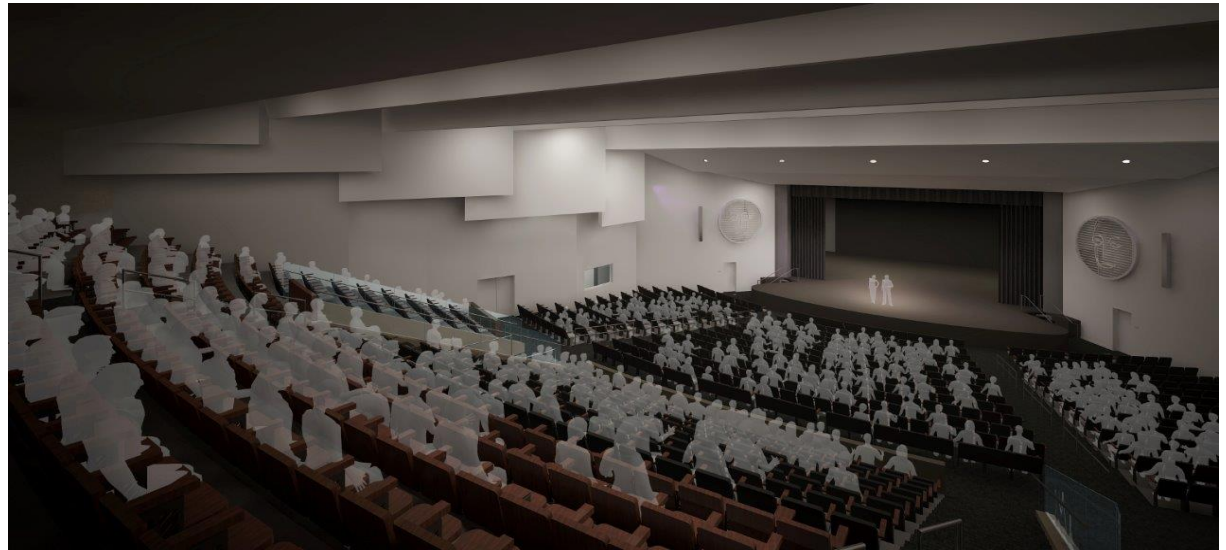

Long Beach Unified School District
