




**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
State: Active					10/1/14	6/28/30				
Phase: OFA					7/20/17	9/23/20				
Project Name: Fire Alarms/Life Safety Sys - Pha					7/20/17	9/15/18				
Construction - Monroe	Fire Alarms/Life Safety Sys - Phase III	All	Alex Main	OFA	7/20/17	12/31/17				
Construction - Marshall	Fire Alarms/Life Safety Sys - Phase III	All	Alex Main	OFA	9/1/17	9/14/18				
Construction - Cubberly/King	Fire Alarms/Life Safety Sys - Phase III	All	Alex Main	OFA	9/1/17	9/15/18				
Project Name: Fire Alarms/Life Safety Sys - Pha					11/12/18	11/15/19				
Construction	Fire Alarms/Life Safety Sys - Phase IV	All	Alex Main	OFA	11/12/18	11/15/19				
Project Name: Fire Alarms/Life Safety Sys - Pha					9/24/19	9/23/20				
Construction	Fire Alarms/Life Safety Sys - Phase V	All	Alex Main	OFA	9/24/19	9/23/20				
Phase: OICS					8/1/16	12/18/19				
Project Name: ICS					8/1/16	12/18/19				
Construction	ICS	ALL	Mickey Kim	OICS	8/1/16	12/18/19				
Phase: OS					8/22/18	3/29/19				
Project Name: Security Improvements					8/22/18	3/29/19				
Construction	Security Improvements	ALL	Mickey Kim	OS	8/22/18	3/29/19				
Phase: OW					9/22/17	1/31/19				
Project Name: E Rate 2016 / 2017					9/22/17	8/31/18				
Construction	E Rate 2016 / 2017	ALL	Mickey Kim	OW	9/22/17	8/31/18				
Project Name: E Rate 2018 / 2019					10/1/18	1/31/19				
Construction	E Rate 2018 / 2019	ALL	Mickey Kim	OW	10/1/18	1/31/19				
Phase: 1					10/1/14	7/8/19				
Project Name: Browning HS New Construction					10/1/14	11/15/18				
Construction	Browning HS New Construction	F	Richard Camacho	1	10/1/14	12/28/17				
Owner Move-in	Browning HS New Construction	F	Richard Camacho	1	7/31/17	1/11/18				
Additional Construction - Site and off-site Work	Browning HS New Construction	F	Richard Camacho	1	12/29/17	11/15/18				
Project Name: Jordan HS Ph 1C, 1D & 4					10/18/17	7/8/19				
Construction	Jordan HS Ph 1C, 1D & 4	A	Jason King	1	10/18/17	4/19/19				
Owner Move-in	Jordan HS Ph 1C, 1D & 4	A	Jason King	1	6/24/19	7/8/19				
Project Name: Kettering ES Interim Housing					10/19/17	2/20/18				
Construction	Kettering ES Interim Housing	F	Richard Camacho	1	10/19/17	2/20/18				
Owner Move-in	Kettering ES Interim Housing	F	Richard Camacho	1	12/16/17	1/3/18				
Project Name: Poly HS ADA Improvements					6/19/17	9/28/18				
Construction	Poly HS ADA Improvements	E	Dan Barr	1	6/19/17	9/28/18				
Project Name: Renaissance HS					9/6/16	12/28/18				
Construction	Renaissance HS	E	Dan Barr	1	9/6/16	12/28/18				
Owner Move-in	Renaissance HS	E	Dan Barr	1	7/16/18	7/27/18				
Project Name: Wilson HS Track/Field					9/18/17	4/9/18				
Construction	Wilson HS Track/Field	F	Richard Camacho	1	9/18/17	3/30/18				
Owner Move-in	Wilson HS Track/Field	F	Richard Camacho	1	4/3/18	4/9/18				
Phase: 2					12/20/17	12/27/18				
Project Name: Cleveland ES HVAC					1/3/18	8/23/18				
Construction	Cleveland ES HVAC	B	James Warmuth	2	1/3/18	8/13/18				
Owner Move-in	Cleveland ES HVAC	B	James Warmuth	2	8/21/18	8/23/18				
Project Name: Garfield ES HVAC					2/6/18	12/27/18				
Construction - Phase 1 (Site, Bldgs C & E)	Garfield ES HVAC	D	Raymond Esparza	2	2/6/18	7/15/18				
Construction - Phase 2 (Bldgs A, D, & F)	Garfield ES HVAC	D	Raymond Esparza	2	7/16/18	8/24/18				
Owner Move-in - Phase 1	Garfield ES HVAC	D	Raymond Esparza	2	8/13/18	8/19/18				
Owner Move-in - Phase 2	Garfield ES HVAC	D	Raymond Esparza	2	8/20/18	8/28/18				
Construction - Phase 3	Garfield ES HVAC	D	Raymond Esparza	2	8/27/18	11/16/18				
Owner Move-in - Phase 3	Garfield ES HVAC	D	Raymond Esparza	2	12/22/18	12/27/18				
Project Name: Kettering ES HVAC					2/5/18	11/14/18				
Construction - Classroom Buildings	Kettering ES HVAC	F	Richard Camacho	2	2/5/18	8/14/18				
Owner Move-in - Phase 1	Kettering ES HVAC	F	Richard Camacho	2	6/16/18	6/22/18				
Construction - Site Work	Kettering ES HVAC	F	Richard Camacho	2	8/15/18	11/14/18				
Owner Move-in - Phase 2	Kettering ES HVAC	F	Richard Camacho	2	8/18/18	8/30/18				

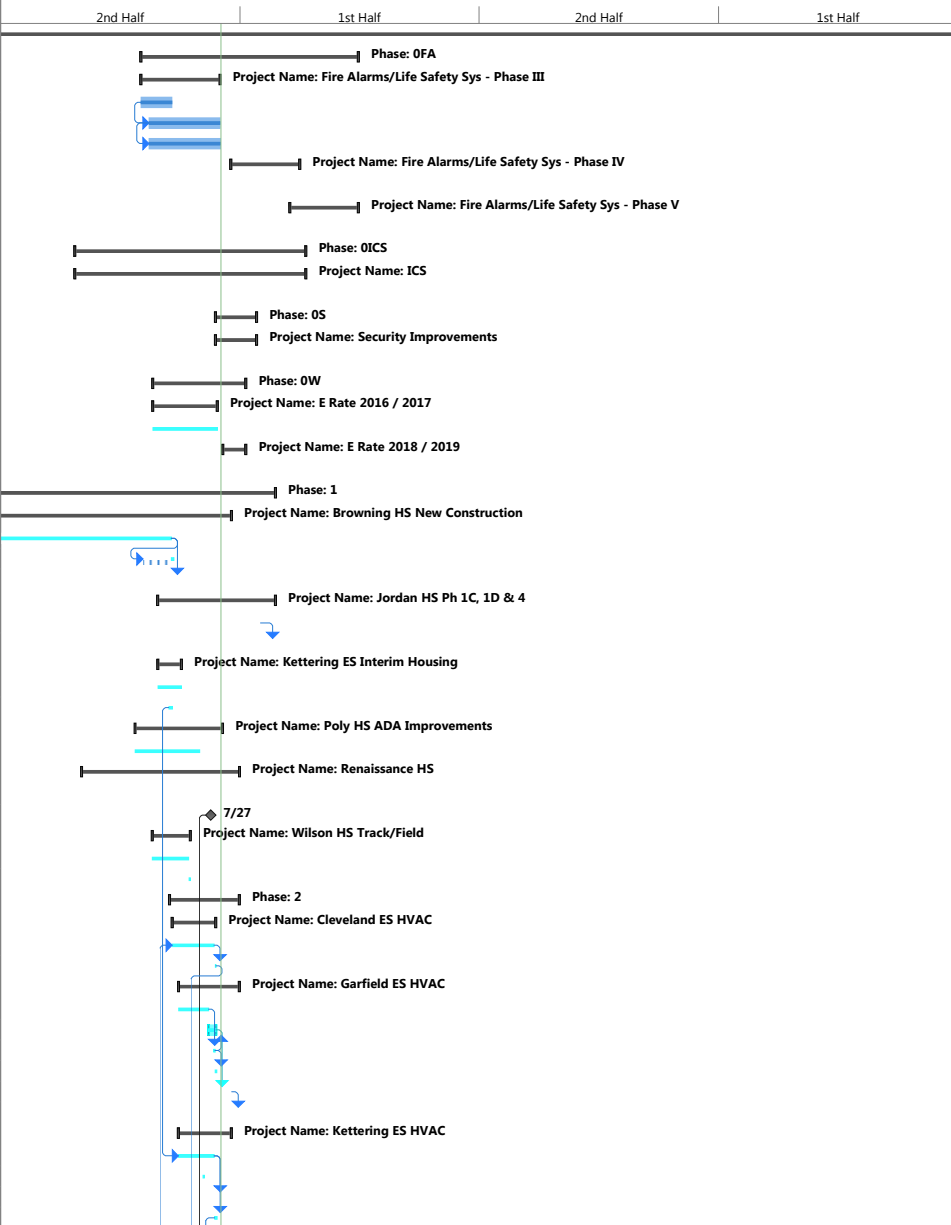

Project updates
Date: 9/21/18

Task	Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Project Name: Poly HS Track/Field					12/20/17	9/10/18				
Construction	Poly HS Track/Field	E	Dan Barr	2	12/20/17	8/24/18				
Owner Move-in	Poly HS Track/Field	E	Dan Barr	2	9/10/18	9/10/18				
Project Name: Riley ES HVAC					1/3/18	12/23/18				
Construction - Classroom Building	Riley ES HVAC	B	James Warmuth	2	1/3/18	8/10/18				
Construction - Site Work	Riley ES HVAC	B	James Warmuth	2	8/11/18	12/23/18				
Owner Move-in	Riley ES HVAC	B	James Warmuth	2	8/14/18	8/20/18				
Project Name: Rogers MS HVAC					2/12/18	8/27/18				
Construction	Rogers MS HVAC	F	Richard Camacho	2	2/12/18	8/14/18				
Owner Move-in	Rogers MS HVAC	F	Richard Camacho	2	8/15/18	8/27/18				
Project Name: Rogers MS Track/Field					6/18/18	8/27/18				
Construction	Rogers MS Track/Field	F	Richard Camacho	2	6/18/18	8/24/18				
Owner Move-in	Rogers MS Track/Field	F	Richard Camacho	2	8/27/18	8/27/18				
Project Name: Stephens MS HVAC					2/9/18	8/30/18				
Construction	Stephens MS HVAC	D	Raymond Esparza	2	2/9/18	8/17/18				
Owner Move-in (furniture)	Stephens MS HVAC	D	Raymond Esparza	2	7/23/18	8/30/18				
Owner Move-in - final	Stephens MS HVAC	D	Raymond Esparza	2	8/13/18	8/18/18				
Project Name: Stephens MS Track/Field					4/16/18	10/1/18				
Construction	Stephens MS Track/Field	D	Raymond Esparza	2	4/16/18	9/17/18				
Owner Move-in	Stephens MS Track/Field	D	Raymond Esparza	2	9/18/18	10/1/18				
Project Name: Webster ES Interim Housing					1/3/18	8/11/18				
Construction	Webster ES Interim Housing	D	Raymond Esparza	2	1/3/18	7/30/18				
Owner Move-in	Webster ES Interim Housing	D	Raymond Esparza	2	7/31/18	8/11/18				
Phase: 3					6/11/18	6/28/30				
Project Name: Barton ES HVAC					6/18/18	7/1/19				
Construction - Phase 1	Barton ES HVAC	A	Jason King	3	6/18/18	12/20/18				
Owner Move-in Phase 1	Barton ES HVAC	A	Jason King	3	12/21/18	1/3/19				
Construction - Phase 2	Barton ES HVAC	A	Jason King	3	1/4/19	6/17/19				
Owner Move-in Phase 2	Barton ES HVAC	A	Jason King	3	6/18/19	7/1/19				
Project Name: Burcham ES HVAC					6/25/18	8/15/19				
Construction	Burcham ES HVAC	C	Tari Fowler	3	6/25/18	8/15/19				
Owner Move-in - Phase 1	Burcham ES HVAC	C	Tari Fowler	3	11/17/18	11/18/18				
Owner Move-in - Phase 2	Burcham ES HVAC	C	Tari Fowler	3	4/20/19	4/26/19				
Project Name: Jefferson MS HVAC					9/10/18	8/29/19				
Construction	Jefferson MS HVAC	F	Richard Camacho	3	9/10/18	8/15/19				
Owner Move-in	Jefferson MS HVAC	F	Richard Camacho	3	8/16/19	8/29/19				
Project Name: Jefferson MS Track/Field					12/1/18	7/16/19				
Construction	Jefferson MS Track/Field	F	Richard Camacho	3	12/1/18	7/1/19				
Owner Move-in	Jefferson MS Track/Field	F	Richard Camacho	3	7/2/19	7/16/19				
Project Name: Jordan HS Ph 2A (Bldgs 100/400)					10/25/18	8/29/19				
Construction	Jordan HS Ph 2A (Bldgs 100/400)	A	Jason King	3	10/25/18	8/15/19				
Owner Move-in	Jordan HS Ph 2A (Bldgs 100/400)	A	Jason King	3	8/16/19	8/29/19				
Project Name: Keller MS Conversion					9/12/18	8/29/19				
Construction	Keller MS Conversion	C	Tari Fowler	3	9/12/18	8/29/19				
Owner Move-in - Phase 1	Keller MS Conversion	C	Tari Fowler	3	2/15/19	2/17/19				
Owner Move-in - Phase 2	Keller MS Conversion	C	Tari Fowler	3	8/17/19	8/23/19				
Project Name: Keller MS Modernization					9/12/18	8/29/19				
Construction	Keller MS Modernization	C	Tari Fowler	3	9/12/18	8/29/19				
Owner Move-in - Phase 1	Keller MS Modernization	C	Tari Fowler	3	2/15/19	2/18/19				
Owner Move-in - Phase 2	Keller MS Modernization	C	Tari Fowler	3	8/17/19	8/23/19				
Project Name: Lakewood HS HVAC					6/14/18	1/13/20				
Construction	Lakewood HS HVAC	B	James Warmuth	3	6/14/18	12/30/19				
Owner Move-in - Phase 1	Lakewood HS HVAC	B	James Warmuth	3	7/1/19	7/15/19				
Owner Move-in - Phase 2	Lakewood HS HVAC	B	James Warmuth	3	12/31/19	1/13/20				
Project Name: Lindsey MS HVAC (Bldg D)					6/18/18	1/4/19				
Construction	Lindsey MS HVAC (Bldg D)	A	Jason King	3	6/18/18	12/21/18				
Owner Move-in	Lindsey MS HVAC (Bldg D)	A	Jason King	3	12/22/18	1/4/19				

Project updates
Date: 9/21/18

Task Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half	
Project Name: Longfellow ES HVAC									Project Name: Longfellow ES HVAC		
Construction - Auditorium	Longfellow ES HVAC	E	Dan Barr	3	6/17/18	8/27/19					
Construction - Classrooms	Longfellow ES HVAC	E	Dan Barr	3	7/2/18	6/18/19					
Owner Move-In - Phase 1	Longfellow ES HVAC	E	Dan Barr	3	12/22/18	12/27/18					
Owner Move-in - Phase 2	Longfellow ES HVAC	E	Dan Barr	3	6/19/19	7/2/19					
Owner Move-in Phase 3	Longfellow ES HVAC	E	Dan Barr	3	8/21/19	8/27/19					
Project Name: Lowell ES HVAC									Project Name: Lowell ES HVAC		
Construction	Lowell ES HVAC	F	Richard Camacho	3	9/10/18	8/29/19					
Owner Move-in (Classrooms building)	Lowell ES HVAC	F	Richard Camacho	3	6/14/19	6/20/19					
Owner Move-in (Non-Classrooms)	Lowell ES HVAC	F	Richard Camacho	3	8/16/19	8/29/19					
Project Name: MacArthur ES HVAC									Project Name: MacArthur ES HVAC		
Construction - Bldgs B & C	MacArthur ES HVAC	B	James Warmuth	3	6/25/18	11/9/18					
Owner Move-in Bldgs B & C	MacArthur ES HVAC	B	James Warmuth	3	11/12/18	11/16/18					
Construction - Bldg A	MacArthur ES HVAC	B	James Warmuth	3	11/17/18	4/19/19					
Owner Move-in Bldg A	MacArthur ES HVAC	B	James Warmuth	3	4/22/19	4/26/19					
Construction - Bldgs D & E	MacArthur ES HVAC	B	James Warmuth	3	4/29/19	8/23/19					
Owner Move-in Bldgs D & E	MacArthur ES HVAC	B	James Warmuth	3	8/26/19	8/30/19					
Project Name: Mann ES HVAC									Project Name: Mann ES HVAC		
Construction	Mann ES HVAC	F	Richard Camacho	3	9/4/18	8/22/19					
Owner Move-In - Phase 1	Mann ES HVAC	F	Richard Camacho	3	12/22/18	1/4/19					
Owner Move-in - Phase 2	Mann ES HVAC	F	Richard Camacho	3	6/18/19	7/1/19					
Owner Move-in - Phase 3	Mann ES HVAC	F	Richard Camacho	3	8/16/19	8/22/19					
Project Name: McKinley ES HVAC									Project Name: McKinley ES HVAC		
Construction Phase 1	McKinley ES HVAC	A	Jason King	3	6/18/18	12/26/18					
Owner Move-in Phase 1	McKinley ES HVAC	A	Jason King	3	12/27/18	1/10/19					
Construction Phase 2	McKinley ES HVAC	A	Jason King	3	1/11/19	6/26/19					
Owner Move-in Phase 2	McKinley ES HVAC	A	Jason King	3	6/27/19	7/11/19					
Project Name: Millikan HS New 1000 Bldg									Project Name: Millikan HS New 1000 Bldg		
Construction	Millikan HS New 1000 Bldg	C	Leslie Sydnor	3	1/2/19	9/1/20					
Owner Move-in	Millikan HS New 1000 Bldg	C	Leslie Sydnor	3	8/1/20	8/21/20					
Project Name: Poly HS Bleachers and Field Light									Project Name: Poly HS Bleachers and Field Lighting		
Construction	Poly HS Bleachers and Field Lighting	E	Brooke Clements	3	10/22/18	5/10/19					
Project Name: Sato HS New Bldg									Project Name: Sato HS New Bldg		
Construction	Sato HS New Bldg	F	Richard Camacho	3	6/11/18	6/19/19					
Owner Move-in	Sato HS New Bldg	F	Richard Camacho	3	6/6/19	6/19/19					
Project Name: Webster ES HVAC									Project Name: Webster ES HVAC		
Construction - Phase 1	Webster ES HVAC	D	Raymond Esparza	3	8/7/18	6/28/30					
Construction - Phase 2	Webster ES HVAC	D	Raymond Esparza	3	6/7/19	8/9/19					
Owner Move-in Phase 1	Webster ES HVAC	D	Raymond Esparza	3	6/17/19	6/28/30					
Owner Move-in Phase 2	Webster ES HVAC	D	Raymond Esparza	3	8/12/19	8/23/19					
Phase: 4									Phase: 4		
Project Name: Alvarado ES HVAC									Project Name: Alvarado ES HVAC		
Construction	Alvarado ES HVAC	E	Brooke Clements	4	6/17/19	6/30/20					
Owner Move-in	Alvarado ES HVAC	E	Brooke Clements	4	6/17/20	6/30/20					
Project Name: Bixby ES HVAC									Project Name: Bixby ES HVAC		
Construction	Bixby ES HVAC	F	Jacquelyn Roberts	4	7/2/19	8/7/20					
Owner Move-in - Phase 1	Bixby ES HVAC	F	Jacquelyn Roberts	4	4/11/20	4/17/20					
Owner Move-in - Phase 2	Bixby ES HVAC	F	Jacquelyn Roberts	4	6/17/20	6/30/20					
Owner Move-in Phase 3	Bixby ES HVAC	F	Jacquelyn Roberts	4	8/3/20	8/7/20					
Project Name: Cubberly K8 Modernization									Project Name: Cubberly K8 Modernization		
Construction	Cubberly K8 Modernization	C	Leslie Sydnor	4	7/12/19	7/22/20					
Owner Move-in	Cubberly K8 Modernization	C	Leslie Sydnor	4	7/9/20	7/22/20					
Project Name: Hamilton MS Gym Measure K									Project Name: Hamilton MS Gym Measure K		
Construction	Hamilton MS Gym Measure K	A	Tracy Nishihira	4	1/22/20	4/23/21					
Owner Move-in	Hamilton MS Gym Measure K	A	Tracy Nishihira	4	6/21/21	6/30/21					
Project Name: Hamilton MS Track & Field									Project Name: Hamilton MS Track & Field		
Construction	Hamilton MS Track & Field	A	Tracy Nishihira	4	8/9/19	5/5/20					

Project updates
Date: 9/21/18

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in	Hamilton MS Track & Field	A	Tracy Nishihira	4	4/22/20	5/5/20				
Project Name: Hughes MS HVAC					6/17/19	9/17/20				
Construction - Phase 1	Hughes MS HVAC	E	Brooke Clements	4	6/17/19	9/18/19				
Construction - Phase 2	Hughes MS HVAC	E	Brooke Clements	4	7/12/19	9/17/20				
Owner Move-in	Hughes MS HVAC	E	Brooke Clements	4	7/20/20	7/31/20				
Project Name: Hughes MS Track/Field					7/12/19	1/7/21				
Construction	Hughes MS Track/Field	E	Brooke Clements	4	7/12/19	10/20/20				
Owner Move-in	Hughes MS Track/Field	E	Brooke Clements	4	12/28/20	1/7/21				
Project Name: Jordan HS Ph 2B & 3					8/15/19	7/19/21				
Construction - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3	A	Tracy Nishihira	4	8/15/19	7/5/21				
Construction - 3 (Bldg 1000)	Jordan HS Ph 2B & 3	A	Tracy Nishihira	4	7/15/20	4/5/21				
Owner Move-in - 3 (Bldg 1000)	Jordan HS Ph 2B & 3	A	Tracy Nishihira	4	4/6/21	4/12/21				
Owner Move-in - 2B (Bldg 200/300)	Jordan HS Ph 2B & 3	A	Tracy Nishihira	4	7/6/21	7/19/21				
Project Name: Madison ES HVAC					4/5/19	6/11/20				
Construction - non-classroom work	Madison ES HVAC	B	James Fortunes	4	4/5/19	5/7/20				
Construction - Classrooms	Madison ES HVAC	B	James Fortunes	4	6/19/19	5/28/20				
Owner Move-in - Phase 1	Madison ES HVAC	B	James Fortunes	4	4/11/20	4/17/20				
Owner Move-in - Phase 2	Madison ES HVAC	B	James Fortunes	4	5/29/20	6/11/20				
Project Name: Millikan HS Track/Field					6/19/19	1/13/20				
Construction	Millikan HS Track/Field	C	Leslie Sydnor	4	6/19/19	12/30/19				
Owner Move-in	Millikan HS Track/Field	C	Leslie Sydnor	4	12/31/19	1/13/20				
Project Name: Muir K8 HVAC					6/24/19	7/7/20				
Construction	Muir K8 HVAC	D	Elston Soares	4	6/24/19	6/23/20				
Owner Move-in	Muir K8 HVAC	D	Elston Soares	4	6/24/20	7/7/20				
Project Name: Naples ES Modernization					6/21/19	1/6/20				
Construction	Naples ES Modernization	F	Jacquelyn Roberts	4	6/21/19	12/20/19				
Owner Move-in	Naples ES Modernization	F	Jacquelyn Roberts	4	12/23/19	1/6/20				
Project Name: Prisk ES Modernization					4/22/19	6/3/20				
Construction	Prisk ES Modernization	C	Leslie Sydnor	4	4/22/19	5/20/20				
Owner Move-in	Prisk ES Modernization	C	Leslie Sydnor	4	5/21/20	6/3/20				
Project Name: Wilson HS HVAC					6/18/19	8/31/21				
Construction	Wilson HS HVAC	F	Jacquelyn Roberts	4	6/18/19	7/30/21				
Owner Move-in	Wilson HS HVAC	F	Jacquelyn Roberts	4	8/2/21	8/31/21				
Phase: 5					2/3/20	10/26/21				
Project Name: Avalon K-12 HVAC					6/15/20	7/16/21				
Construction	Avalon K-12 HVAC	D	Elston Soares	5	6/15/20	7/2/21				
Owner Move-in	Avalon K-12 HVAC	D	Elston Soares	5	7/5/21	7/16/21				
Project Name: Bancroft MS HVAC					6/1/20	3/30/21				
Construction - Phase 1	Bancroft MS HVAC	B	James Fortunes	5	6/1/20	8/31/20				
Construction - Phase 2	Bancroft MS HVAC	B	James Fortunes	5	8/3/20	3/16/21				
Owner Move-in	Bancroft MS HVAC	B	James Fortunes	5	3/17/21	3/30/21				
Project Name: Birney ES Modernization					6/15/20	6/28/21				
Construction - Phase 1	Birney ES Modernization	E	Brooke Clements	5	6/15/20	9/14/20				
Construction - Phase 2	Birney ES Modernization	E	Brooke Clements	5	7/8/20	6/14/21				
Owner Move-in	Birney ES Modernization	E	Brooke Clements	5	6/15/21	6/28/21				
Project Name: Fremont ES HVAC					7/1/20	6/28/21				
Construction	Fremont ES HVAC	F	Jacquelyn Roberts	5	7/1/20	6/14/21				
Owner Move-in - Phase 1	Fremont ES HVAC	F	Jacquelyn Roberts	5	4/3/21	4/9/21				
Owner Move-in - Phase 2	Fremont ES HVAC	F	Jacquelyn Roberts	5	6/15/21	6/28/21				
Project Name: Holmes ES HVAC					5/29/20	6/10/21				
Construction	Holmes ES HVAC	B	James Fortunes	5	5/29/20	5/26/21				
Owner Move-in - Phase 1	Holmes ES HVAC	B	James Fortunes	5	4/3/21	4/9/21				
Owner Move-in - Phase 2	Holmes ES HVAC	B	James Fortunes	5	5/28/21	6/10/21				
Project Name: Keller MS New Locker Room					2/3/20	2/16/21				
Construction	Keller MS New Locker Room	C	Leslie Sydnor	5	2/3/20	2/2/21				
Owner Move-in	Keller MS New Locker Room	C	Leslie Sydnor	5	2/3/21	2/16/21				


Project updates
Date: 9/21/18

Task Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half		1st Half		2nd Half		1st Half	
Project Name: Lakewood HS Track/Field					5/20/20	2/17/21								
Construction	Lakewood HS Track/Field	B	James Fortunes	5	5/20/20	1/19/21								
Owner Move-in	Lakewood HS Track/Field	B	James Fortunes	5	1/20/21	2/17/21								
Project Name: Millikan HS Modernization					6/9/20	10/26/21								
Construction	Millikan HS Modernization	C	Leslie Sydnor	5	6/9/20	10/12/21								
Owner Move-in	Millikan HS Modernization	C	Leslie Sydnor	5	10/13/21	10/26/21								
Project Name: Stanford MS HVAC					7/10/20	7/21/21								
Construction	Stanford MS HVAC	C	Leslie Sydnor	5	7/10/20	7/7/21								
Owner Move-in Phase 1	Stanford MS HVAC	C	Leslie Sydnor	5	12/21/20	1/1/21								
Owner Move-in Phase 2	Stanford MS HVAC	C	Leslie Sydnor	5	7/8/21	7/21/21								
Project Name: Stanford MS Track/Field					7/10/20	1/22/21								
Construction	Stanford MS Track/Field	C	Leslie Sydnor	5	7/10/20	1/8/21								
Owner Move-in	Stanford MS Track/Field	C	Leslie Sydnor	5	1/11/21	1/22/21								
Project Name: Twain ES HVAC					6/1/20	7/9/21								
Construction - Phase 1	Twain ES HVAC	B	James Fortunes	5	6/1/20	8/31/20								
Construction - Phase 2	Twain ES HVAC	B	James Fortunes	5	7/23/20	6/25/21								
Owner Move-in - Phase 1	Twain ES HVAC	B	James Fortunes	5	4/3/21	4/9/21								
Owner Move-in - Phase 2	Twain ES HVAC	B	James Fortunes	5	6/28/21	7/9/21								
Project Name: Washington MS HVAC					6/15/20	7/16/21								
Construction	Washington MS HVAC	D	Elston Soares	5	6/15/20	7/2/21								
Owner Move-in	Washington MS HVAC	D	Elston Soares	5	7/5/21	7/16/21								
Project Name: Washington MS Track/Field					6/15/20	7/16/21								
Construction	Washington MS Track/Field	D	Elston Soares	5	6/15/20	7/2/21								
Owner Move-in	Washington MS Track/Field	D	Elston Soares	5	7/5/21	7/16/21								
Phase: 6					6/3/20	9/30/24								
Project Name: Bancroft MS Track/Field					6/3/20	3/1/21								
Construction	Bancroft MS Track/Field	B	James Fortunes	6	6/3/20	2/15/21								
Owner Move-in	Bancroft MS Track/Field	B	James Fortunes	6	2/16/21	3/1/21								
Project Name: Beach HS Modernization					6/14/21	7/26/22								
Construction	Beach HS Modernization	F	Jacquelyn Roberts	6	6/14/21	7/12/22								
Owner Move-in	Beach HS Modernization	F	Jacquelyn Roberts	6	7/13/22	7/26/22								
Project Name: Bryant ES Modernization					6/29/21	1/12/22								
Construction	Bryant ES Modernization	F	Jacquelyn Roberts	6	6/29/21	12/29/21								
Owner Move-in	Bryant ES Modernization	F	Jacquelyn Roberts	6	12/30/21	1/12/22								
Project Name: Emerson ES Modernization					7/12/21	7/18/22								
Construction	Emerson ES Modernization	C	Leslie Sydnor	6	7/12/21	7/4/22								
Owner Move-in	Emerson ES Modernization	C	Leslie Sydnor	6	7/5/22	7/18/22								
Project Name: Gant ES Modernization					7/8/21	7/14/22								
Construction (Non Classrooms)	Gant ES Modernization	F	Jacquelyn Roberts	6	7/8/21	6/30/22								
Owner Move-in	Gant ES Modernization	F	Jacquelyn Roberts	6	7/1/22	7/14/22								
Project Name: Gompers K8 Modernization					5/28/21	6/9/22								
Construction	Gompers K8 Modernization	B	James Fortunes	6	5/28/21	5/26/22								
Owner Move-in	Gompers K8 Modernization	B	James Fortunes	6	5/27/22	6/9/22								
Project Name: Hoover MS HVAC					7/16/21	8/12/22								
Construction	Hoover MS HVAC	B	James Fortunes	6	7/16/21	7/14/22								
Owner Move-in	Hoover MS HVAC	B	James Fortunes	6	7/15/22	8/12/22								
Project Name: Jordan HS Ph 5 & 6					7/6/21	9/30/24								
Construction - Gym	Jordan HS Ph 5 & 6	A	Tracy Nishihira	6	7/6/21	10/21/22								
Construction - Pool, Bleachers, Stadium	Jordan HS Ph 5 & 6	A	Tracy Nishihira	6	11/7/22	3/20/24								
Owner Move-in - Gym	Jordan HS Ph 5 & 6	A	Tracy Nishihira	6	3/21/24	4/3/24								
Owner Move-in - Pool, Bleachers, Stadium	Jordan HS Ph 5 & 6	A	Tracy Nishihira	6	3/21/24	4/3/24								
Construction - Fields	Jordan HS Ph 5 & 6	A	Tracy Nishihira	6	4/4/24	9/30/24								
Project Name: Lakewood HS Pool/Nat					1/4/21	2/4/22								
Construction	Lakewood HS Pool/Nat	B	James Fortunes	6	1/4/21	1/21/22								
Owner Move-in	Lakewood HS Pool/Nat	B	James Fortunes	6	1/24/22	2/4/22								
Project Name: Poly HS Multi-Phase					7/16/21	8/8/23								
Construction	Poly HS Multi-Phase	E	Brooke Clements	6	7/16/21	7/25/23								

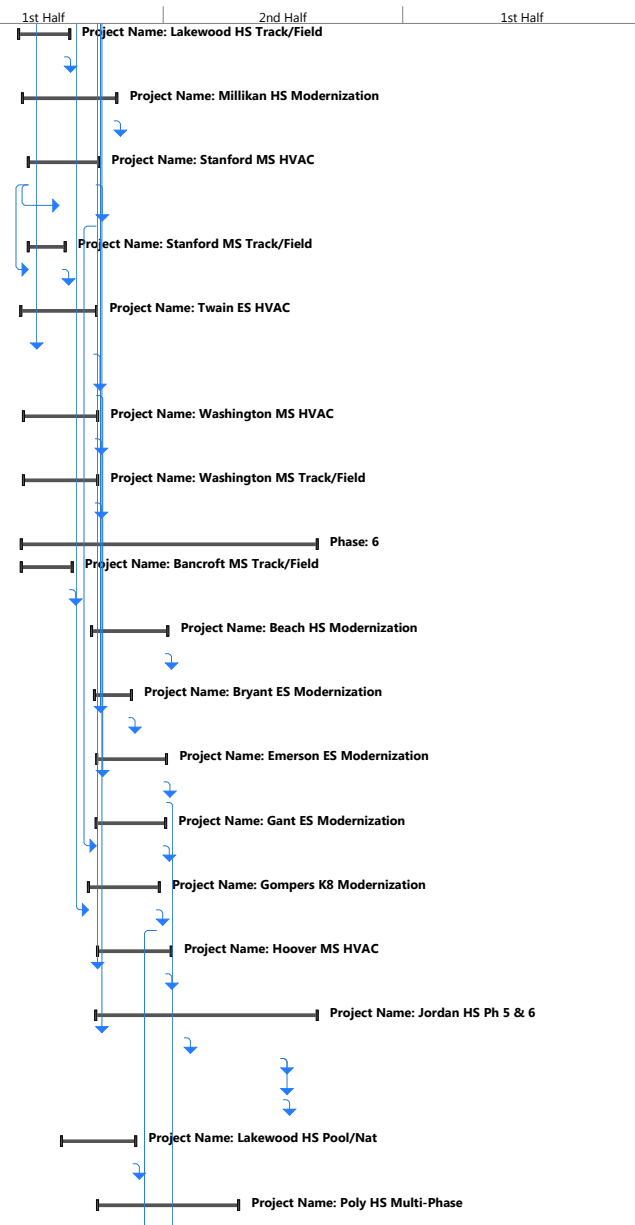


Project updates Date: 9/21/18	Task	Summary
----------------------------------	------	---------



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in	Poly HS Multi-Phase	E	Brooke Clements	6	7/26/23	8/8/23				
Project Name: Sato HS HVAC					6/14/21	8/2/22				
Construction	Sato HS HVAC	F	Jacquelyn Roberts	6	6/14/21	7/19/22				
Owner Move-in	Sato HS HVAC	F	Jacquelyn Roberts	6	7/20/22	8/2/22				
Phase: 7					5/20/21	8/23/23				
Project Name: Gompers K8 Track/Field					5/17/22	11/7/22				
Construction	Gompers K8 Track/Field	B	James Fortunes	7	5/17/22	10/31/22				
Owner Move-in	Gompers K8 Track/Field	B	James Fortunes	7	11/1/22	11/7/22				
Project Name: Hoover MS Track/Field					11/30/22	8/15/23				
Construction	Hoover MS Track/Field	B	James Fortunes	7	11/30/22	8/1/23				
Owner Move-in	Hoover MS Track/Field	B	James Fortunes	7	8/2/23	8/15/23				
Project Name: Los Cerritos ES Modernization					5/27/22	5/25/23				
Construction	Los Cerritos ES Modernization	E	Brooke Clements	7	5/27/22	5/11/23				
Owner Move-in	Los Cerritos ES Modernization	E	Brooke Clements	7	5/12/23	5/25/23				
Project Name: Marshall MS Modernization					8/17/22	8/23/23				
Construction	Marshall MS Modernization	C	Leslie Sydnor	7	8/17/22	8/9/23				
Owner Move-in	Marshall MS Modernization	C	Leslie Sydnor	7	8/10/23	8/23/23				
Project Name: Newcomb K8 Track/Field					3/15/22	11/29/22				
Construction	Newcomb K8 Track/Field	C	Leslie Sydnor	7	3/15/22	11/15/22				
Owner Move-in	Newcomb K8 Track/Field	C	Leslie Sydnor	7	11/16/22	11/29/22				
Project Name: Sato HS Track/Field					5/20/21	2/2/22				
Construction	Sato HS Track/Field	F	Jacquelyn Roberts	7	5/20/21	1/19/22				
Owner Move-in	Sato HS Track/Field	F	Jacquelyn Roberts	7	1/20/22	2/2/22				
Project Name: Tincher K8 Modernization					7/19/22	8/7/23				
Construction	Tincher K8 Modernization	F	Jacquelyn Roberts	7	7/19/22	7/24/23				
Owner Move-in	Tincher K8 Modernization	F	Jacquelyn Roberts	7	7/25/23	8/7/23				
Project Name: Wilson HS Pool/Nat					5/20/21	5/26/22				
Construction	Wilson HS Pool/Nat	F	Jacquelyn Roberts	7	5/20/21	5/12/22				
Owner Move-in	Wilson HS Pool/Nat	F	Jacquelyn Roberts	7	5/13/22	5/26/22				
Phase: 8					5/12/23	10/9/24				
Project Name: Carver ES Modernization					5/12/23	5/17/24				
Construction	Carver ES Modernization	C	Leslie Sydnor	8	5/12/23	5/3/24				
Owner Move-in	Carver ES Modernization	C	Leslie Sydnor	8	5/6/24	5/17/24				
Project Name: Franklin MS Track/Field					1/18/24	9/19/24				
Construction	Franklin MS Track/Field	E	Brooke Clements	8	1/18/24	9/18/24				
Owner Move-in	Franklin MS Track/Field	E	Brooke Clements	8	9/19/24	9/19/24				
Project Name: Henry ES HVAC					8/8/23	8/19/24				
Construction	Henry ES HVAC	B	James Fortunes	8	8/8/23	8/5/24				
Owner Move-in - Phase 1	Henry ES HVAC	B	James Fortunes	8	3/10/24	3/22/24				
Owner Move-in - Phase 2	Henry ES HVAC	B	James Fortunes	8	8/6/24	8/19/24				
Project Name: Lindberg MS Track/Field					7/10/23	3/8/24				
Construction	Lindberg MS Track/Field	A	Tracy Nishihira	8	7/10/23	3/8/24				
Owner Move-in	Lindberg MS Track/Field	A	Tracy Nishihira	8	7/10/23	7/23/23				
Project Name: Marshall MS Track/Field					1/25/24	10/9/24				
Construction	Marshall MS Track/Field	C	Leslie Sydnor	8	1/25/24	9/25/24				
Owner Move-in	Marshall MS Track/Field	C	Leslie Sydnor	8	9/26/24	10/9/24				
Project Name: Millikan HS Pool/Nat					5/23/23	7/29/24				
Construction	Millikan HS Pool/Nat	C	Leslie Sydnor	8	5/23/23	7/15/24				
Owner Move-in	Millikan HS Pool/Nat	C	Leslie Sydnor	8	7/16/24	7/29/24				
Phase: 9					9/2/24	10/3/25				
Project Name: Poly HS Pool/Nat					9/2/24	10/3/25				
Construction	Poly HS Pool/Nat	E	Brooke Clements	9	9/2/24	9/19/25				
Owner Move-in	Poly HS Pool/Nat	E	Brooke Clements	9	9/22/25	10/3/25				
Phase: 10					4/11/25	8/6/26				
Project Name: Buffum TK HVAC					6/18/25	6/24/26				
Construction	Buffum TK HVAC	F	Jacquelyn Roberts	10	6/18/25	6/10/26				

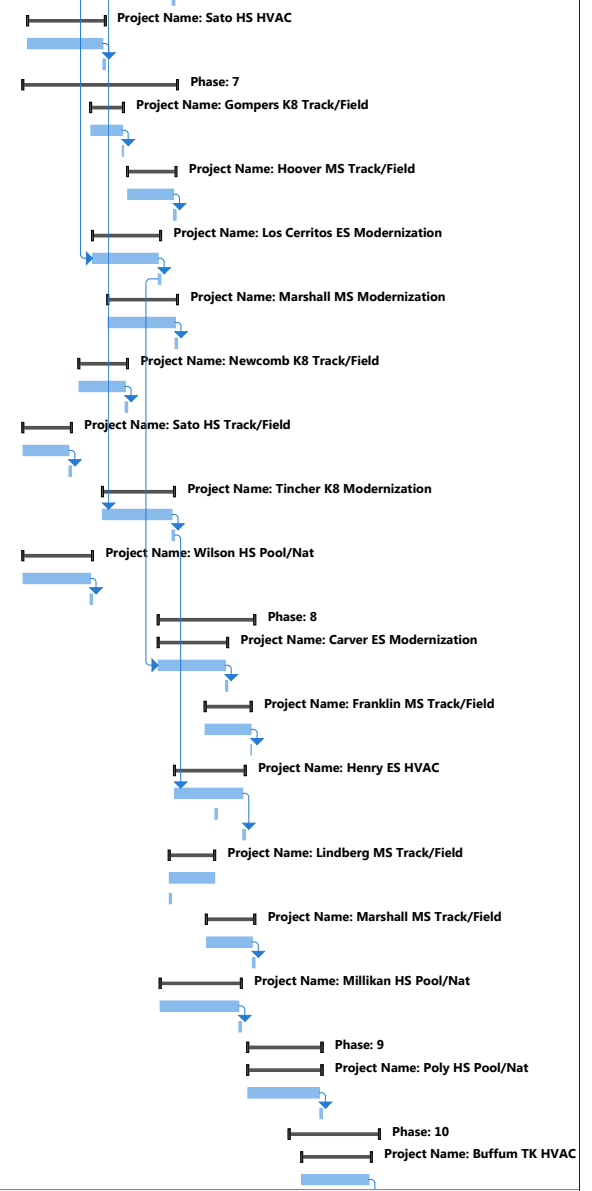

Project updates
Date: 9/21/18

Task Summary



**LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018**

Task Name	Project Name	Reg	RESP	Phase	Start	Finish	2nd Half	1st Half	2nd Half	1st Half
Owner Move-in	Buffum TK HVAC	F	Jacquelyn Roberts	10	6/11/26	6/24/26				
Project Name: Hudson K-8 Track/Field										
Construction	Hudson K-8 Track/Field	D	Elston Soares	10	6/5/25	11/19/25				
Owner Move-in	Hudson K-8 Track/Field	D	Elston Soares	10	11/6/25	11/19/25				
Project Name: Monroe MOD										
Construction	Monroe MOD	B	James Fortunes	10	11/21/25	8/6/26				
Owner Move-in	Monroe MOD	B	James Fortunes	10	7/24/26	8/6/26				
Project Name: Powell K8 Track/Field										
Construction	Powell K8 Track/Field	A	Tracy Nishihira	10	4/11/25	8/8/25				
Project Name: Tucker SpEd HVAC										
Construction	Tucker SpEd HVAC	F	Jacquelyn Roberts	10	6/15/25	7/3/26				
Owner Move-in	Tucker SpEd HVAC	F	Jacquelyn Roberts	10	6/22/26	7/3/26				
State: Complete					1/6/15	7/3/18				
Phase: OFA					6/30/16	6/30/17				
Project Name: Fire Alarms/Life Safety Sys - Pha										
Construction	Fire Alarms/Life Safety Sys - Phase II	All	Alex Main	OFA	6/30/16	6/30/17				
Phase: OSC					7/6/17	1/30/18				
Project Name: Security Camera Phase II										
Construction	Security Camera Phase II	ALL	Mickey Kim	OSC	7/6/17	1/30/18				
Phase: OW					1/4/18	4/4/18				
Project Name: Wireless Phase V										
Construction	Wireless Phase V	ALL	Mickey Kim	OW	1/4/18	4/4/18				
Phase: 1					1/6/15	7/3/18				
Project Name: Barton/Educare ES										
Construction	Barton/Educare ES	A	Raymond Esparza	1	2/24/17	7/3/18				
Owner Move-in	Barton/Educare ES	A	Raymond Esparza	1	7/2/18	7/3/18				
Project Name: Cabrillo HS Track/Field										
Construction	Cabrillo HS Track/Field	D	James Warmuth	1	6/15/17	10/26/17				
Owner Move-in	Cabrillo HS Track/Field	D	James Warmuth	1	11/14/17	11/28/17				
Project Name: Head Start at Bethune										
Construction	Head Start at Bethune	D	James Warmuth	1	3/8/18	5/14/18				
Owner Move-in	Head Start at Bethune	D	James Warmuth	1	5/8/18	5/14/18				
Project Name: Head Start at Hudson										
Construction	Head Start at Hudson	D	James Warmuth	1	10/23/17	4/12/18				
Owner Move-in	Head Start at Hudson	D	James Warmuth	1	4/12/18	4/12/18				
Project Name: Head Start at Jordan Plus										
Construction	Head Start at Jordan Plus	A	James Warmuth	1	10/24/17	5/8/18				
Owner Move-in	Head Start at Jordan Plus	A	James Warmuth	1	5/8/18	5/8/18				
Project Name: Monroe K8 Interim Housing										
Construction	Monroe K8 Interim Housing	B	Raymond Esparza	1	7/21/17	12/26/17				
Owner Move-in	Monroe K8 Interim Housing	B	Raymond Esparza	1	12/22/17	12/26/17				
Project Name: Poly HS Auditorium										
Construction	Poly HS Auditorium	E	Dan Barr	1	1/6/15	10/26/17				
Owner Move-in	Poly HS Auditorium	E	Dan Barr	1	10/23/17	11/2/17				
Project Name: Poly HS Band Bldg Conversion V										
Construction	Poly HS Band Bldg Conversion Work	E	Dan Barr	1	10/23/17	11/14/17				
Owner Move-in	Poly HS Band Bldg Conversion Work	E	Dan Barr	1	11/15/17	11/16/17				
Project Name: Riley ES Interim Housing										
Construction	Riley ES Interim Housing	B	Raymond Esparza	1	10/20/17	12/22/17				
Owner Move-in	Riley ES Interim Housing	B	Raymond Esparza	1	12/27/17	12/28/17				
Project Name: Rogers MS Portables										
Construction	Rogers MS Portables	F	Richard Camacho	1	10/16/17	12/7/17				
Owner Move-in	Rogers MS Portables	F	Richard Camacho	1	12/29/17	12/31/17				
Project Name: Sato HS Conversion										
Construction	Sato HS Conversion	F	Richard Camacho	1	6/5/17	9/8/17				
Owner Move-in	Sato HS Conversion	F	Richard Camacho	1	8/1/17	8/18/17				

Project updates
Date: 9/21/18





LONG BEACH UNIFIED SCHOOL DISTRICT
EXECUTIVE PROGRAM SCHEDULE as of 8/31/2018

Task Name	Project Name	Reg	RESP	Phase	Start	Finish				
Project Name: Sato HS Gym										
Construction	Sato HS Gym	F	Richard Camacho	1	5/23/16	1/31/18		2nd Half	1st Half	
Owner Move-in	Sato HS Gym	F	Richard Camacho	1	8/21/17	1/8/18		2nd Half		1st Half
Project Name: Wilson HS Auditorium										
Construction	Wilson HS Auditorium	F	Richard Camacho	1	2/22/16	3/6/18		2nd Half	1st Half	
Owner Move-in	Wilson HS Auditorium	F	Richard Camacho	1	2/21/18	3/6/18		2nd Half		1st Half

Project updates
Date: 9/21/18

Task Summary

This schedule is a reflection of the anticipated project execution and completion dates at the time of printing. These dates are subject to change depending on many factors including DSA design approvals, unforeseen delays, and bonds fund availability.
