

Jordan High School
CM Services: Phase 1B
Construction Activities
 Update: December 16th, 2016

Progress Photos



Building J: 2nd Floor Corridor



Building K: Classroom



Building L: 2nd Floor Classroom




Building J: Piano Room



Building K: Classroom



Building L: 2nd Floor Classroom

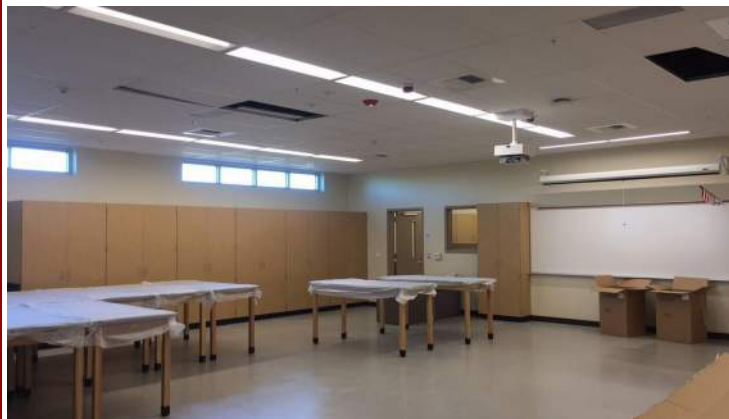

Building J: Classroom



Building K: Classroom



Building L: 1st Floor Classroom



Building J: Classroom

Building J: Final cleaning, door hardware, and window coverings are in progress. Flooring in the 1st floor Black Box is wrapping up. Cable trays in the TV Studio is underway. Expansion joint cover assemblies are being installed at Stair #2.

Building K: Carpet and door hardware are ongoing throughout the building. Miscellaneous casework activities are ongoing and will soon wrap up. Ceiling tile will finish up as soon as the overhead final inspection is approved.

Building L: Above ceiling electrical work and low voltage work is ongoing on the 2nd floor. Carpet installation to begin as soon as it is done in Building K. Toilet partitions and accessories at bathrooms are near completion.

Site Work:

- Parking lot slurry is scheduled for 12/29/16
- Stripping is scheduled for 1/5/17
- Miscellaneous hardware at gates is ongoing
