



### **Project Summary:**

- Existing 64,000 s.f. facility in the Poly Planning area
- Built in 1935 with additions in 1945 and 1966
- 3.8 acre site
- Facilities Master Plan recommended complete campus replacement
- 98,686 s.f. with 45 classrooms
- On-site parking structure for staff with roof top playground

### **Project Status:**

- Final states of construction
- School re-opening: Fall 2015




### **Project Team:**

- Architect: Ghataode Bannon Architects, LLP
- Contractor: Tilden-Coil Constructors, Inc.

### **Budget:**

- Estimated Total Project Budget: \$58.81M
- Estimated Construction Budget: \$49.61M
- Dollars Expended (as of 5/29/15): \$48M

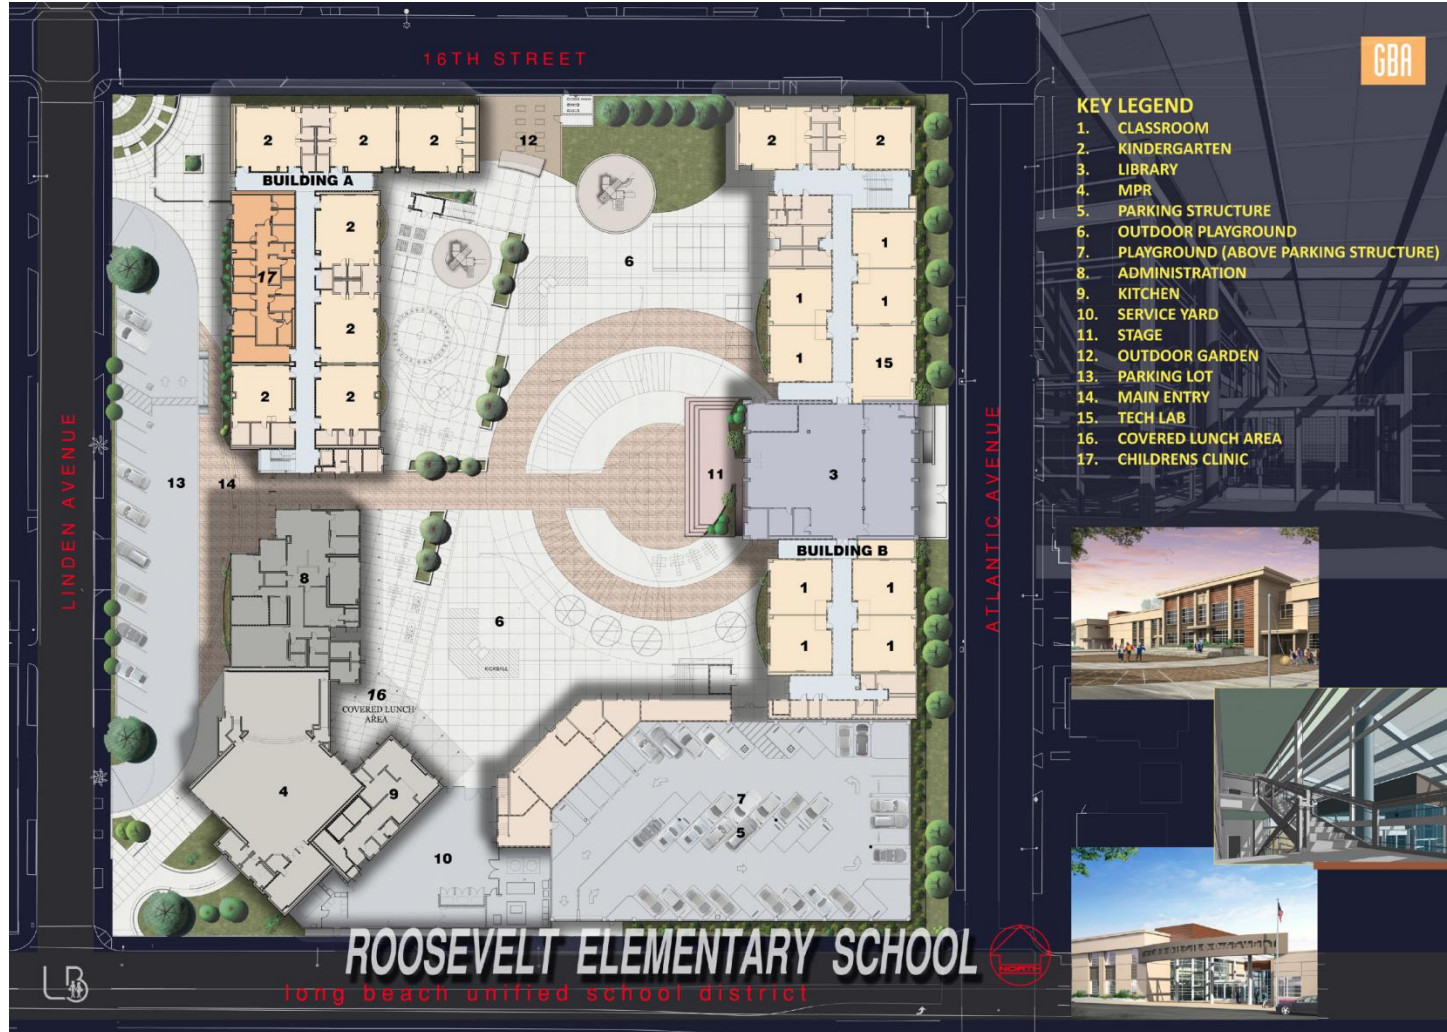



# I. Major Projects Update

## Roosevelt Elementary School New Construction

