



II. Major Projects Update

Renaissance High School for the Arts

Project Summary

- Existing facility constructed in 1930s and additions constructed in the 1940s
- New Performing Arts building and Physical Education facilities
- Renovation of existing buildings
- Removal of portables
- Site accessibility and fire life safety upgrades
- Opening Fall 2018

Project Status

- Design development: Complete
- Interim housing plan: Underway
- Construction documents: Complete

Upcoming Activities

- DSA Submittal: June 11, 2015
- DSA Review: Underway
- DSA Approval: March 2016
- Bidding: April 2016
- Construction: Summer 2016 – 2018



Project Team

- Architect: Ghataode Bannon Architects, LLP
- Contractor: TBD


Budget

- Estimated Total Project Budget: \$40M
- Estimated Construction Budget: \$28.1M
- Dollars Expended (as of 01/13/16): \$1.78M



II. Major Projects Update

Renaissance High School for the Arts

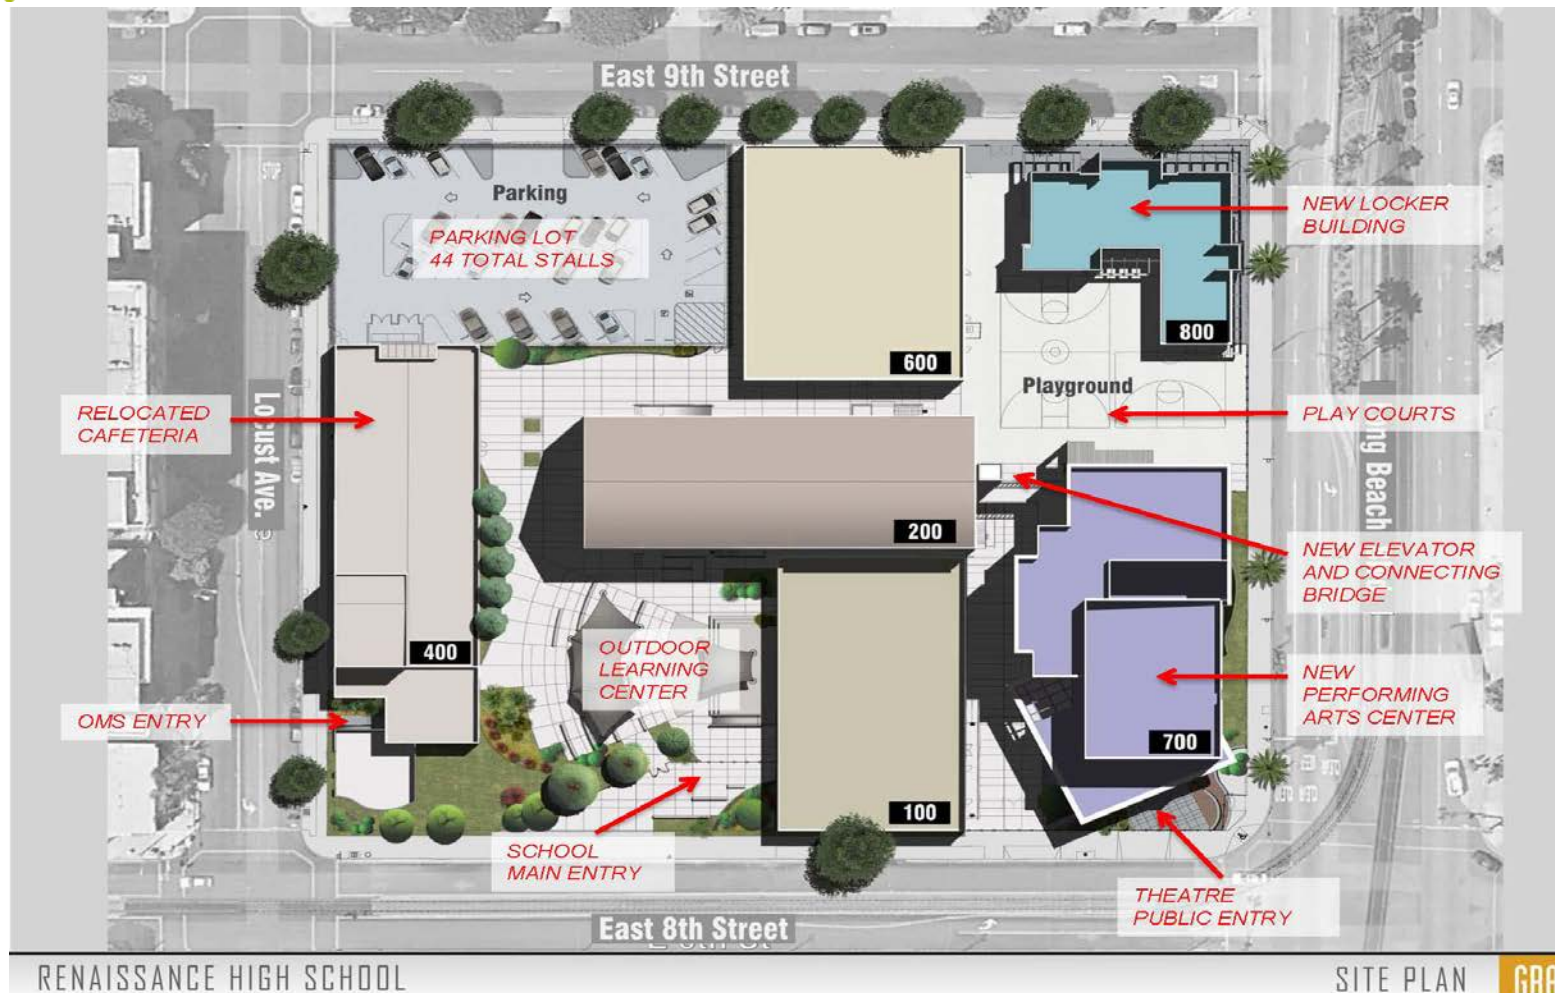

RENAISSANCE HIGH SCHOOL

SITE PLAN

GBA
