



II. Major Projects Update

Jordan High School Major Renovation

Project Summary:


- Existing facilities built in 1930's and 1940's with additions built in the 1950's through 1990's
- 26.89 acre site
- Existing 301,663 s.f. of permanent and 31,680 s.f. of portable structures
- New and renovated facilities: 395,000 s.f.
- 132 classrooms, six (6) Academies
- Master Plan capacity: 3,600 students

Project Status:

- Construction: Ph. 1A Interim Housing (92% complete)
- DSA Agency Review: Ph. 1B Increment 2 and 1C
- Construction Documents: Ph. 2B Underway
- Schematic Design: 5 and 6 Underway
- Schematic Design Complete: 2A and 4
- Phase 1B Demolition: Underway

Upcoming Activities:

- Design Development: 2A : Underway
- Design Development 4: Competed
- Phase 1B Increment 1: Bid Opening September 30, 2014; Start date October 2014

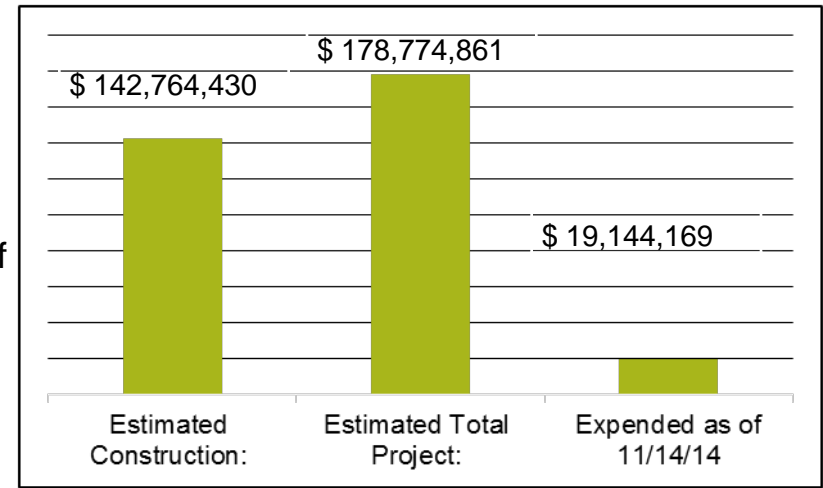

Project Team:

- Architect: NTD (Ph. 1, 2B), and PJHM (Ph. 2A, 4, 5, 6)
- Contractors:
 - Phase 1A: McCarthy Building Companies
 - Phase 1B Demo: Unlimited Environmental
 - Phase 1B inc.1: Haywood Baker
 - Phase 1B inc.2: TBD



II. Major Projects Update

Jordan High School Major Renovation

Jordan HS Education Program


- Learning Laboratories
- Science Laboratories
- Specialized Technical Educational Laboratories
- Special Education Classrooms
- Visual Arts Classrooms
- Teaching Stations
- Administration Building
- Media Center
- Gymnasium
- Multi-Purpose Room
- Food Services
- Common Core Laboratory





II. Major Projects Update

Jordan High School Major Renovation

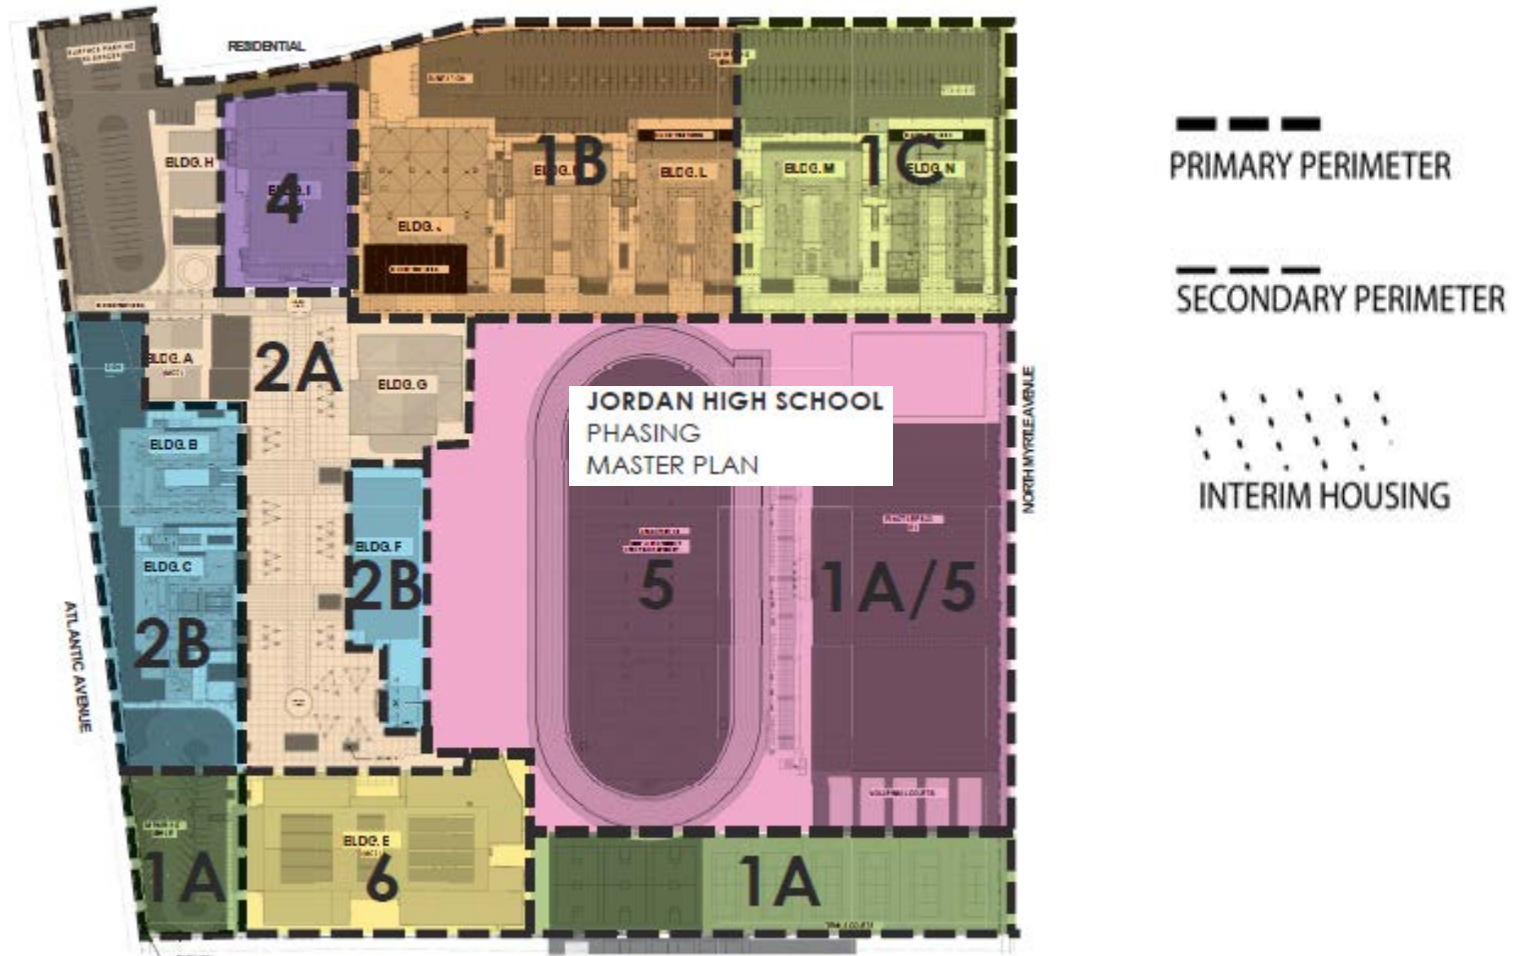



II. Major Projects Update

Jordan High School Major Renovation



Building 850



MEASURE K SCHOOL BONDS
Building for 21st Century Learning

I. Major Projects Update

Jordan High School Major Renovation

