



I. Major Projects Update

New High School #5 - Conversion to Eunice Sato Academy of Mathematics and Science

Project Summary:

- Eunice Sato Academy of Mathematics and Science
- Educational programs in Science, Technology, Engineering and Mathematics
- A phased system will be used to convert existing MS to a HS
- Scope:
 1. Portable demolition
 2. Parking lot expansion
 3. Exterior painting
 4. Minor classroom modifications
 5. Minor fencing
 6. New PE building with locker rooms (AB 300 project)
 7. Demolition of existing gym

Project Status:

- Engineering Computer Labs: Complete
- Classroom Conversion: June 2015 – August 2015
- Portable Demolition & Parking Lot Expansion: June 2015 – August 2015
- Exterior Painting & Wood June 2015 – August 2015

Upcoming Activities:

- Chemistry Lab modifications: Summer 2015
- Fencing: Fall 2015
- Athletic/Locker Facility: Fall 2015
- Demolition of existing Gym: Summer 2016



Project Team:

Architect:

Portable Demolition & Parking Lot Expansion:
Ghataode Bannon Architects, LLP

Contractor:

- Portable Demolition & Parking Lot Expansion: Torres Construction
- Exterior Painting & Wood Repair: Tony's Painting

Budget:*

- Estimated Total Project Budget: \$2.24M
- Estimated Construction Budget: \$1.01M
- Dollars Expended (as of 5/29/15): \$121K



*(Not including new Athletic/Locker Facility and Demolition of existing Gym building)



MEASURE K SCHOOL BONDS
Building for 21st Century Learning

I. Major Projects Update

New High School #5 - Conversion to Eunice Sato
Academy of Mathematics and Science

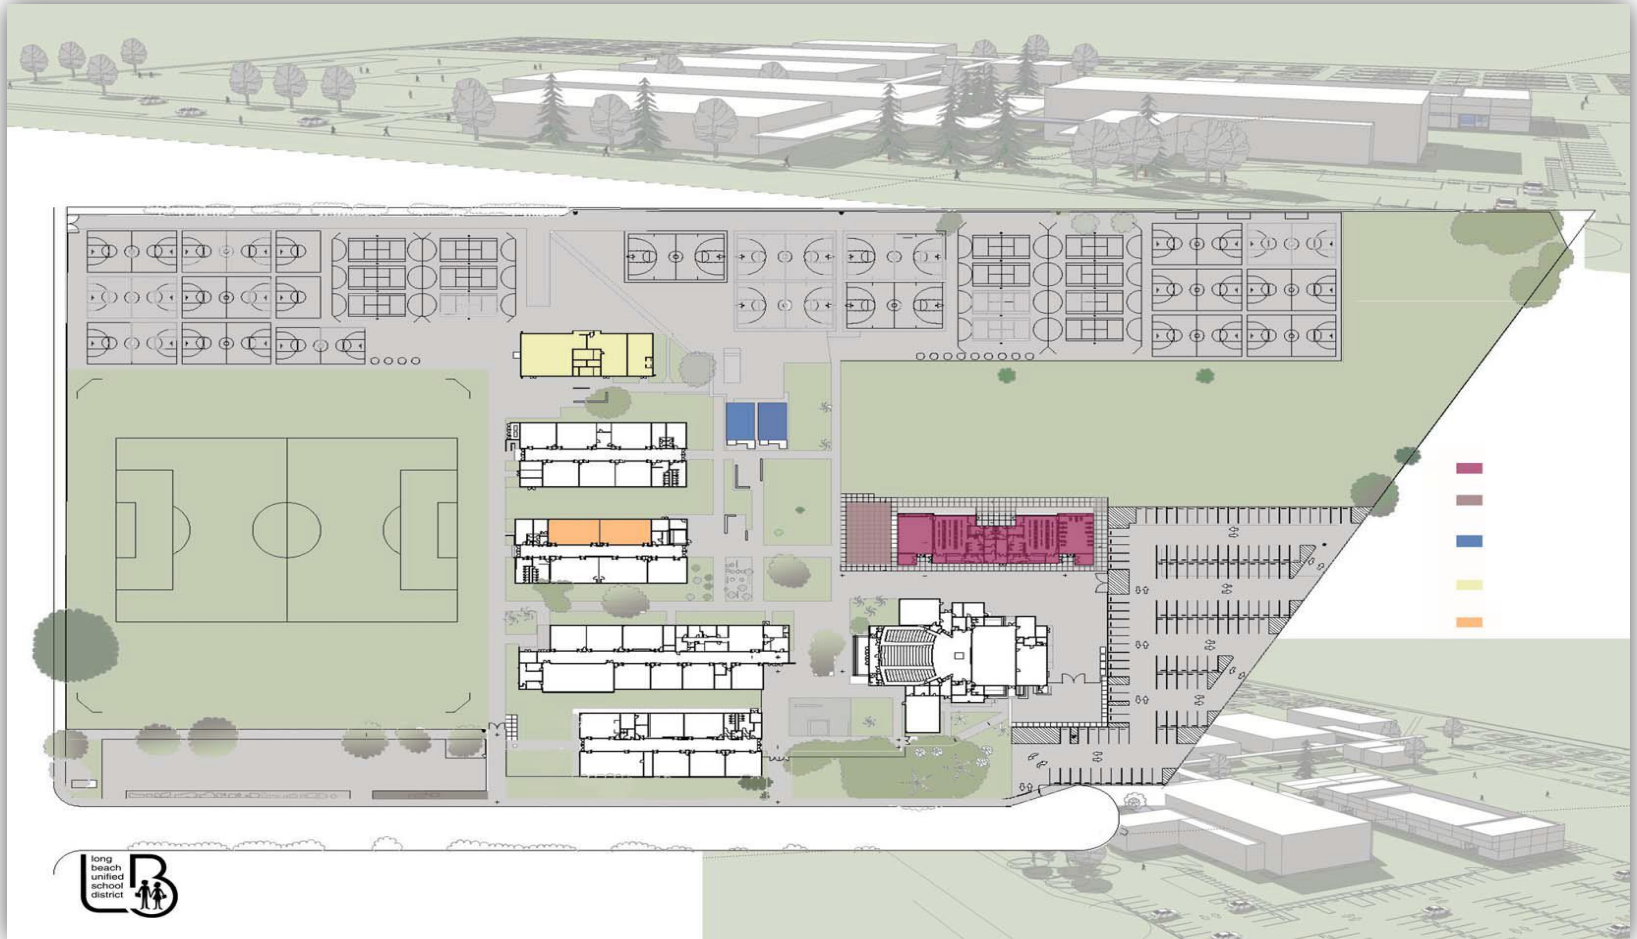

Proposed Site Plan
